



US Army Corps  
of Engineers

# 2011 MISSOURI RIVER LEVEE REHAB UPDATE

MRLS 471 - 460 R  
Doniphan County, Kansas

Updated as of Feb. 21, 2013

Kansas City Residence Office

Kansas City District

## Schedule

Request for Assistance:	Sept. 29, 2011
Damage Survey Report:	Nov. 23, 2011
Award Date:	Feb. 9, 2012
Notice to Proceed Date:	Feb. 21, 2012
Contract Duration:	120
Contract Original Completion Date:	June 20, 2012
Contract Current Completion Date:	June 20, 2012
Estimated Completion Date:	June 20, 2012

## Progress


% Complete Actual:	98%
% Complete Schedule:	98%
Construction Contract Placement:	\$0.00

## Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$767,770.00
Current Contract Amount:	\$767,770.00
Pending MOD Amount:	\$0.00

Project: MRLS 471-460-R

River Miles: 441.9 to 456.6

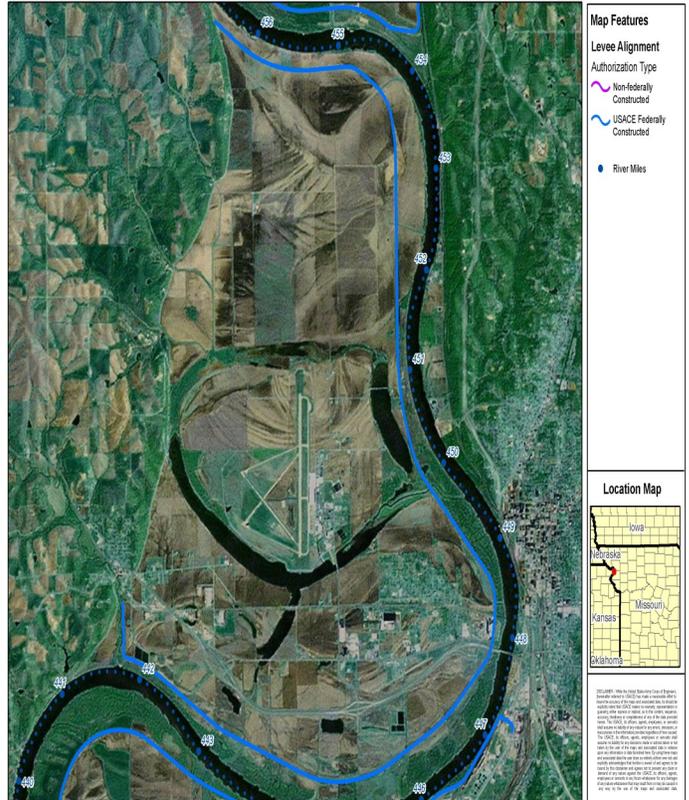

## Scope of work

Embankment scour and foundation seepage repair.

***Current Progress***

Contract awarded on February 9, 2012 to Cajun Contractors. Pre-construction meeting was held at the Kansas City Resident Office on 2/14/12. Notice to proceed acknowledge on 2/21/12.

Cajun remobilized to the site last week to begin debris removal in accordance with their plan. In conflict with their initial plan, and our concerns which we expressed last fall, Cajun has elected to have TL Enterprises complete the reseeding for the third time. We are working with Cajun on a plan to ensure success this time around.

***Photos***
