



2011 MISSOURI RIVER LEVEE REHAB UPDATE

MRLS 440 R

US Army Corps
of Engineers

Atchison / Douglas, Kansas

Updated as of April 24, 2013

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Nov. 7, 2011
Damage Survey Report:	Nov. 23, 2011
Award Date:	July 20, 2012
Notice to Proceed Date:	Aug. 13, 2012
Contract Duration:	180
Contract Original Completion Date:	Dec. 8, 2012
Contract Current Completion Date:	Feb. 16, 2013
Estimated Completion Date:	Feb. 16, 2013


Progress

% Complete Actual:	93%
% Complete Schedule:	93%
Construction Contract Placement:	\$0.00

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$552,420.00
Current Contract Amount:	\$552,420.00
Pending MOD Amount:	\$0.00

Project: MRLS 440-R River Miles: 424 to 431.3

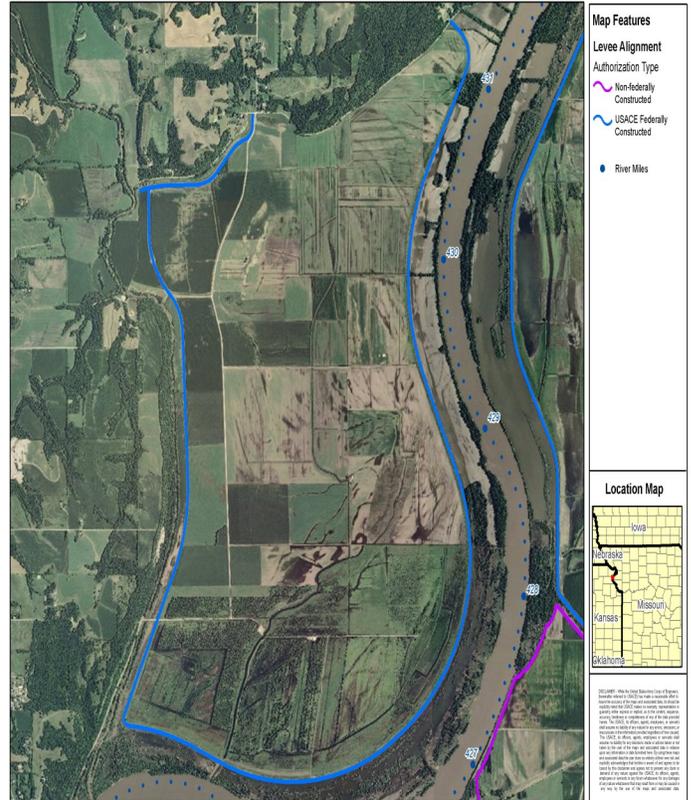

Scope of work

Construct underseepage berms with impervious material to restore the original level of protection by providing weight against uplift and underseepage forces. Backfill and compact scour holes with random and impervious fill. Re-seed and fertilize the zone between the riverside toe of the levee and high water elevation (including stability berms) plus five feet of riverside foreshore.

Current Progress

Contract award of Levee Rehab Contract MRLS R-440 to Klocke, Inc. for \$552,420 on 7/20/12. Notice to Proceed issued 8/13/12.

The earthwork is complete, weather has not allowed an opportunity for seeding. Late spring has prevented much of seed to germinate, making it difficult to determine if the seeding efforts have yielded satisfactory stands of grass to meet the performance establishment criteria.

Photos
