



2011 MISSOURI RIVER LEVEE REHAB UPDATE

MRLS 408 - L

Platte County, Missouri

US Army Corps
of Engineers

Updated as of Oct. 26, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Aug. 4, 2011
Damage Survey Report:	Sept. 1, 2011
Award Date:	Mar 23, 2012
Notice to Proceed Date:	April 5, 2012
Contract Duration:	60
Contract Original Completion Date:	June 3, 2012
Contract Current Completion Date:	June 3, 2012
Estimated Completion Date:	June 3, 2012

Progress


% Complete Actual:	97%
% Complete Schedule:	97%
Construction Contract Placement:	

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	
Current Contract Amount:	
Pending MOD Amount:	

Project: MRLS 408-L

River Miles: 391.4 to 401.7

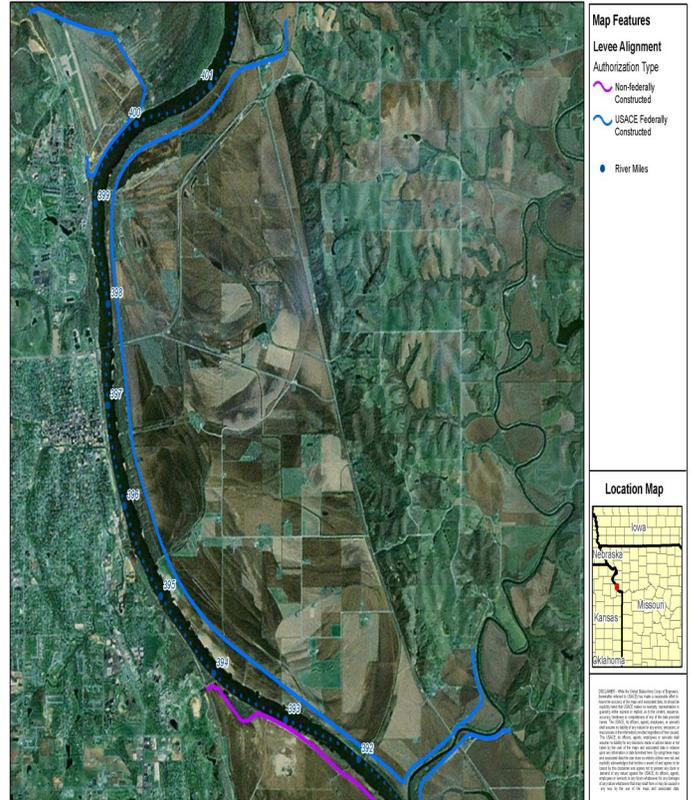

Scope of work

Anticipated work includes placement of seepage berms near stations 521+50 to 523+50 and near stations 470+00 to 475+00. Work also includes backfilling and compacting scour holes. Riverbank slope protection will be accomplished by reseeding and fertilizing the zone between the riverside toe of the levee and the high water elevation plus five feet of foreshore.

Current Progress

Contract Status: The contract was awarded 3/23/2012. The pre-construction meeting was held on 3/27/12. The Mutual Understanding Meeting was held on 3/29/12. Notice to proceed was issued 4/5/12.

TL Enterprises complete seeding of the majority of the levee within the fall seeding window. We will inspect the areas in question in the coming weeks to evaluate the status of the newly planted grass.

Photos
