



US Army Corps  
of Engineers

# 2011 MISSOURI RIVER LEVEE REHAB UPDATE

MRLS 488 - L

Holt County, Missouri

Updated as of Oct. 26, 2012

Kansas City Residence Office

Kansas City District

## Schedule

Request for Assistance:	July 22, 2011
Damage Survey Report:	Nov. 8, 2011
Award Date:	May 22, 2012
Notice to Proceed Date:	May 31, 2012
Contract Duration:	120
Contract Original Completion Date:	Nov. 28, 2012
Contract Current Completion Date:	Nov. 28, 2012
Estimated Completion Date:	Nov. 28, 2012


## Progress

% Complete Actual:	99%
% Complete Schedule:	99%
Construction Contract Placement:	\$0.00

## Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$2,363,808.40
Current Contract Amount:	\$2,363,808.40
Pending MOD Amount:	\$0.00

Project: MRLS 488-L (Holt County District No. 7) River Miles: 465.4 to 476.2

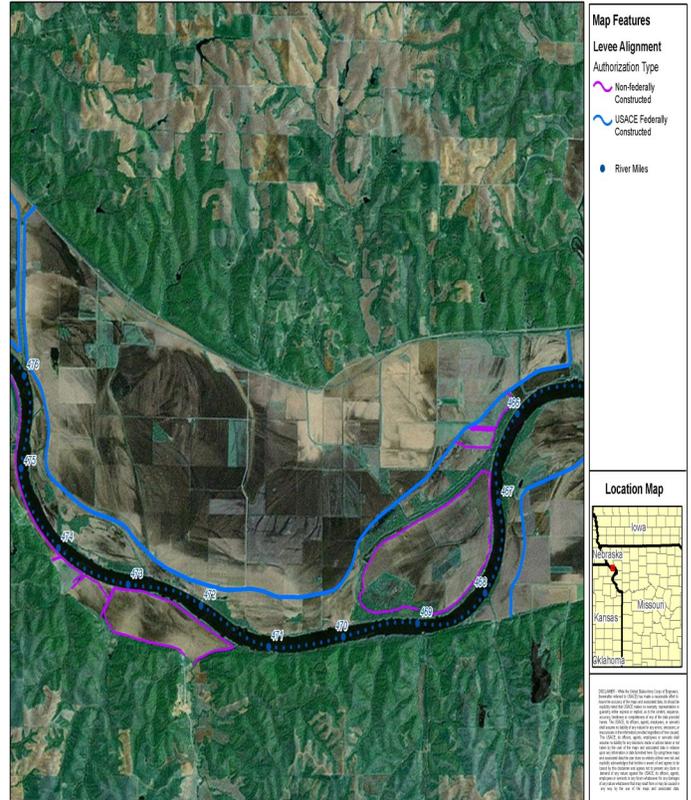

## Scope of work

Anticipated work includes placement of seepage berms near stations 165+00 to 178+00, near stations 195+00 to 210+00, near stations 220+00 to 240+00, near stations 310+00 to 315+00, and near stations 540+00 to 550+00. Work also includes backfilling and compacting numerous scour holes between located between stations 99+49 through 398+70. Riverbank slope protection will be accomplished by reseeding and fertilizing the zone between the riverside toe of the levee and the high water elevation plus 5 feet of foreshore.

***Current Progress***

Contract awarded to Phillips Excavating & Grading for \$2,363,808 on 5/22/12.

We held a pre-final/final inspection of MRLS 488 and accepted the project without deficiencies. Phillips finished all work over a month ahead of schedule. The contractor returned the evaluation today and it has been forwarded to the reviewing official.

***Photos***
