



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Clyde
Clyde, Kansas

Updated as of Nov. 29, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Aug. 8 2011
Damage Survey Report:	Nov. 7, 2011
Award Date:	Apr. 13, 2012
Notice to Proceed Date:	Apr. 27, 2012
Contract Duration:	60
Contract Original Completion Date:	Jun. 26, 2012
Contract Current Completion Date:	Jun. 26, 2012
Estimated Completion Date:	Jun. 26, 2012

Progress

% Complete Actual:	100%
% Complete Schedule:	100%
Construction Contract Placement:	0


Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	
Current Contract Amount:	
Pending MOD Amount:	



Project: Clyde

River Miles: 0.88 to 2.1

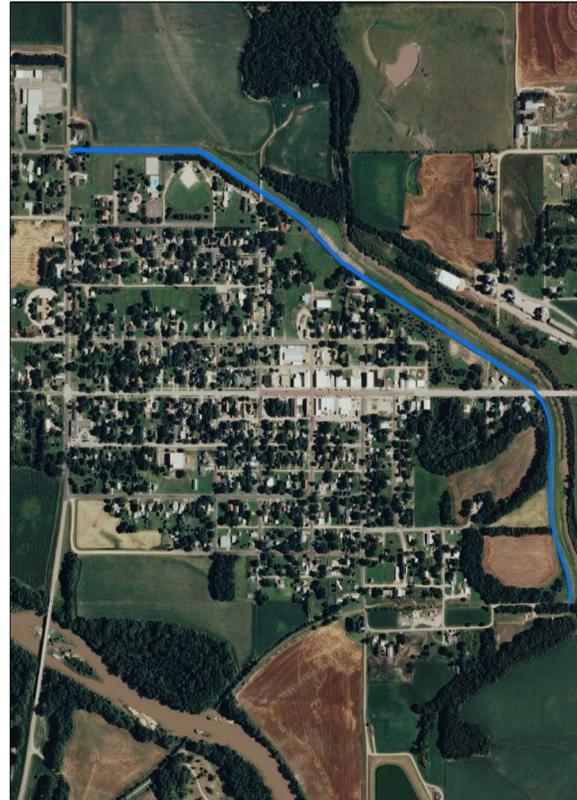

Map Features

Levee Alignment

Authorization Type

~ Non-federally Constructed

~ USACE Federally Constructed

• River Miles

Location Map



08/14/12 - This is a map showing the project location. The map is a satellite image with a blue line indicating the project location. The map is titled 'Project: Clyde' and 'River Miles: 0.88 to 2.1'. The map shows a residential area with houses and trees, and agricultural fields. A legend on the right identifies 'Levee Alignment' and 'Authorization Type' (Non-federally Constructed and USACE Federally Constructed). A 'Location Map' inset shows the project area within the state of Kansas.

Scope of work

Repair erosion on the right bank of the improved Elk Creek Channel through placement of quarry-run rock fill. Approximate repair areas include locations between Stations 25+50 to 26+50 and Stations 37+30 to 39+30.

Current Progress

Contract awarded to Bayer on 4/13/12.

After a few weeks confirming the status of the grass stand, multiple inspections proved it is acceptable to the on-site quality assurance, contractor's Quality Control Manager and the City of Clyde. We are continuing to move forward with closeout and final pay.

Photos
