



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Wolcott Section 2
Wyandotte, Kansas

Updated as of Nov. 29, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	July 30, 2011
Damage Survey Report:	Dec. 27, 2011
Award Date:	May 1, 2012
Notice to Proceed Date:	May 10, 2012
Contract Duration:	110
Contract Original Completion Date:	Aug. 27, 2012
Contract Current Completion Date:	Aug. 27, 2012
Estimated Completion Date:	Aug. 27, 2012


Progress

% Complete Actual:	95%
% Complete Schedule:	95%
Construction Contract Placement:	\$0.00

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$20,632
Current Contract Amount:	\$20,632
Pending MOD Amount:	\$0.00

Project: Wolcott Drainage District Section 2 River Miles: 382.3 to 383.7

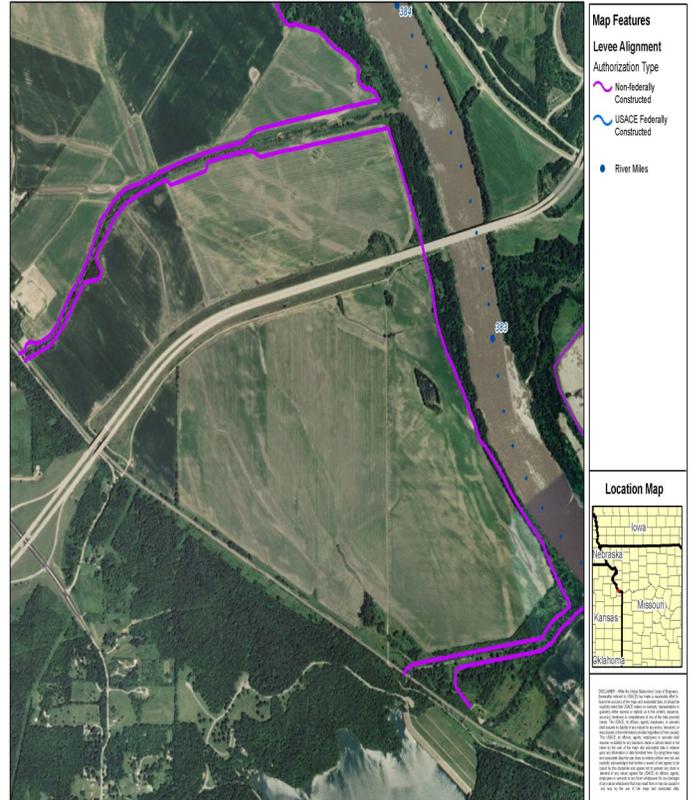

Scope of work

Breach and large scour hole repair.

Current Progress

The contract was awarded 5/1/12 to Prudent Technologies.

Final Inspection was held 11/15/12. Since Prudent seeded outside of the seeding window we will inspect the grass stand again in the weeks prior to the spring seeding window of 2013.

Photos
