



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

MRLS 471 - 460 R
Doniphan County, Kansas

Updated as of April 24, 2013

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Sept. 29, 2011
Damage Survey Report:	Nov. 23, 2011
Award Date:	Feb. 9, 2012
Notice to Proceed Date:	Feb. 21, 2012
Contract Duration:	120
Contract Original Completion Date:	June 20, 2012
Contract Current Completion Date:	June 20, 2012
Estimated Completion Date:	June 20, 2012

Progress

% Complete Actual:	98%
% Complete Schedule:	98%
Construction Contract Placement:	\$0.00


Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$767,770.00
Current Contract Amount:	\$767,770.00
Pending MOD Amount:	\$0.00



Project: MRLS 471-460-R

River Miles: 441.9 to 456.6

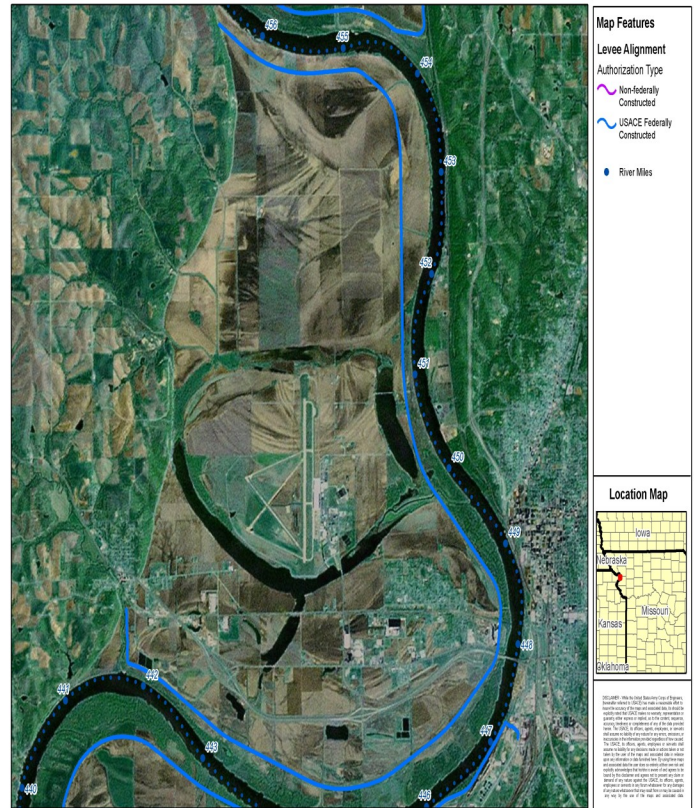

Scope of work

Embankment scour and foundation seepage repair.

Current Progress

Contract awarded on February 9, 2012 to Cajun Contractors. Pre-construction meeting was held at the Kansas City Resident Office on 2/14/12. Notice to proceed acknowledge on 2/21/12.

All re-seeding on the Kansas side has been completed. Cajun had just mobilized to the Missouri side and got one day of work in last week before weather shut them down. As of 4/24/13, it is still too wet to do any seeding. Plan is to resume onsite 4/29/13, after conditions improve. Approximately three days of seeding remains. Some of the first areas they reseeded this spring are beginning to show growth.

Photos
