


Missouri River BSNP Project Maintenance Omaha District

Matt Krajewski

Missouri River Project Office, Omaha NE

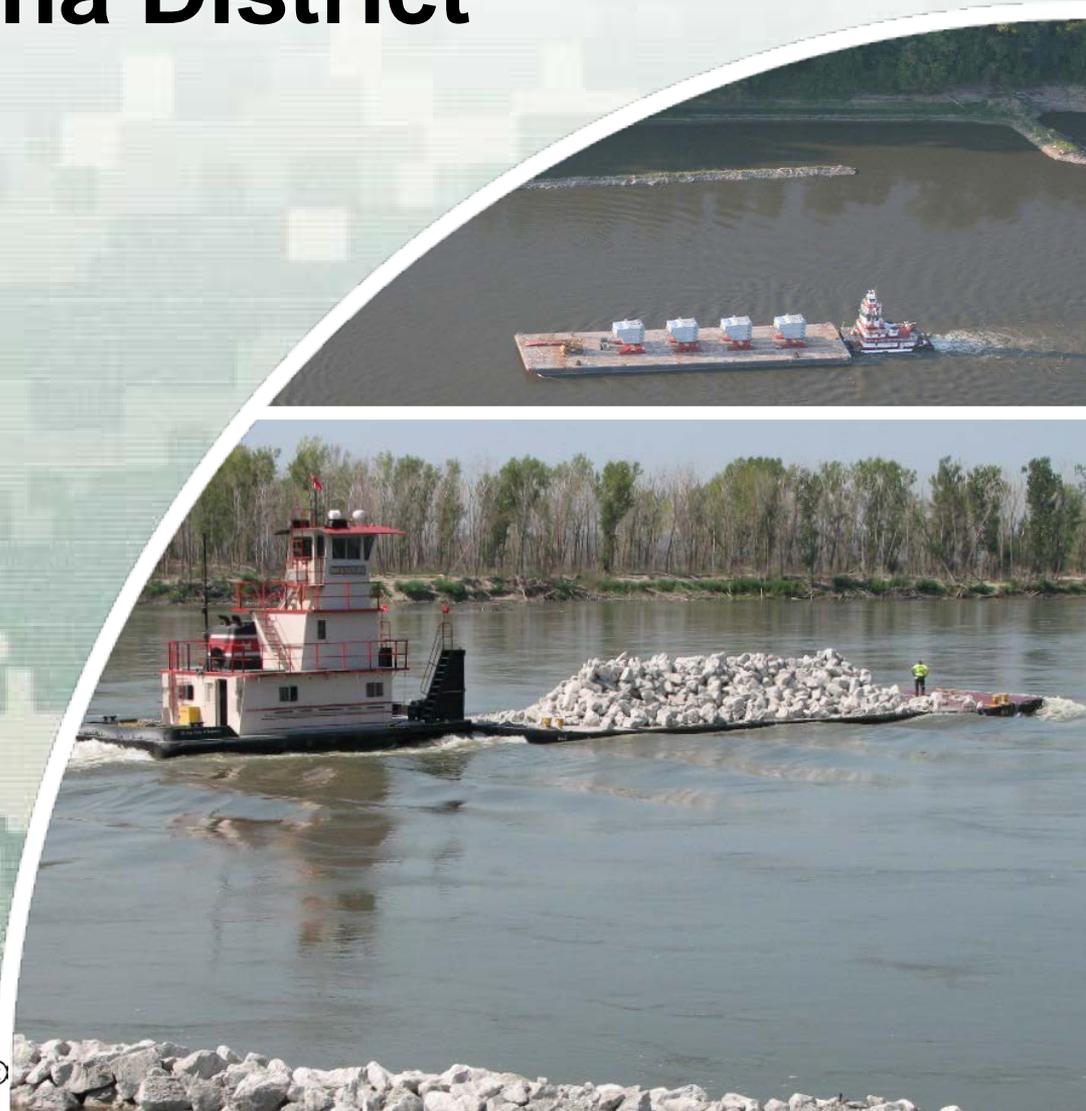

US Army Corps of Engineers
BUILDING STRONG®



®


Missouri River Project Maintenance



Omaha District
Work Crew 2012



Survey of Deroin Bend

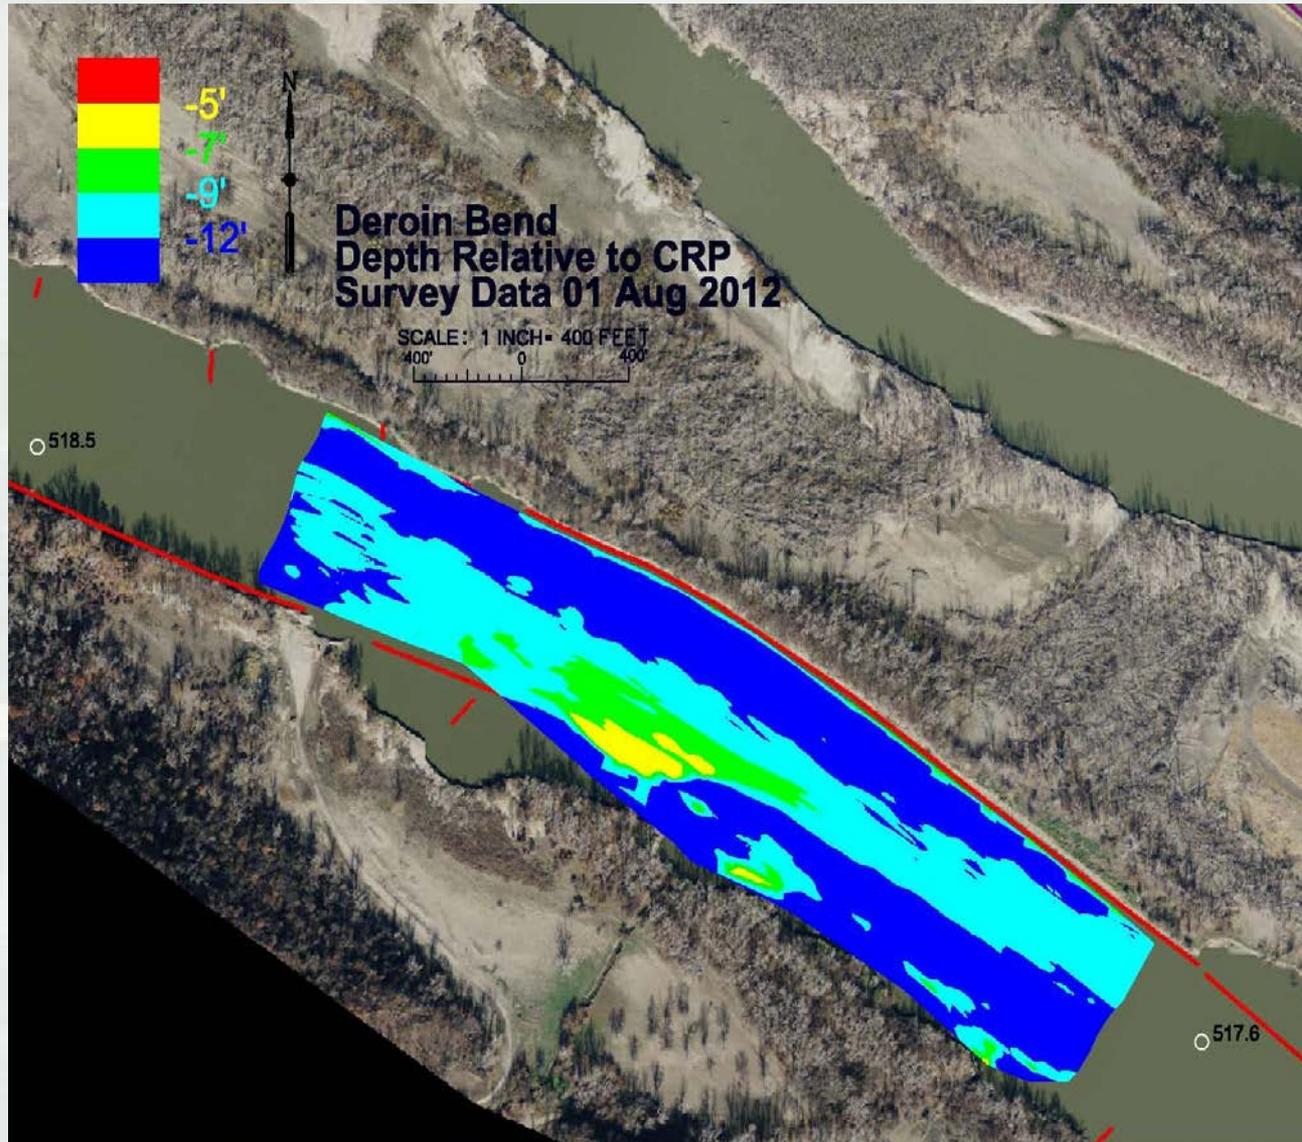

Deroin Bend Proposed Repairs



BUILDING STRONG®

Inlet to Kansas Bend Chute, Mile 546



October 16, 2012



BUILDING STRONG®

Inlet to Lower Hamburg Chute, Mile 553



Lower Hamburg
Inlet 2009

Flow 

October 16, 2012



Restored Revetment - Council Bend Chute

Mile 617



October 16, 2012



BUILDING STRONG®

M/V Tigre Working Revetment Repair

Mile 642 – Desoto Cutoff Bend



October 16, 2012



BUILDING STRONG®

Lower Decatur Bend – Revetment Lowering Shallow Water Habitat Project



DRAA Construction Summary

Project	Award Amount	Contractor	Award Date	Number of Structures	Rock Volume (tons)	Placed FY 12			Estimate FY 13			Estimate FY 14			
						Volume	Amount	Per. Comp.	Volume	Amount	Per. Comp.	Volume	Amount	Per. Comp.	
Upper / Lower Hamburg Closure *	\$1,031,000	BY Excavating (subbed to Western)		2	15,000	15,000	\$1,031,000	100%							
BNSP North Phase 1	\$4,020,700	Newt Marine	8-Jun-12	47	114,850	71,172	\$2,491,609	62%	43,678	\$1,529,091	38%				
BNSP South Phase 1	\$4,288,625	Western	Jun-12	55	135,850	19,118	\$603,533	14%	116,732	\$3,685,092	86%				
BNSP North Phase 2	\$3,559,200	Big River	14-Sep-12	275	102,600	0	\$0	0%	20,520	\$711,840	20%	82,080	\$2,847,360	80%	
BNSP South Phase 2	\$4,514,850	Big River	14-Sep-12	324	145,000	0	\$0	0%	29,000	\$902,970	20%	116,000	\$3,611,880	80%	
Sub Total				\$17,414,375	703	513,300	105,290	\$4,126,142	24%	209,930	\$6,828,993	39%	198,080	\$6,459,240	37%



MRPO Budget Summary

- FY 10 \$1,400,514
- FY 11 \$1,433,000
- FY 12 \$1,988,849
- FY 13 \$1,752,917
- FY 14 \$1,881,937 (Planning Numbers)
- FY 15 \$1,791,293 (Planning Numbers)



Significant Channel Work Planned for 2013

- USACE

- ▶ Focus on completing channel repairs at Lower Decatur Bend: 34,000 tons
- ▶ Other high priority work: 7700 tons
- ▶ Additional 19,500 tons of lower priority work likely will wait until 2014

- By Contract

- ▶ 250k tons already awarded



Questions



BUILDING STRONG®
