


Missouri River BSNP Project Maintenance Omaha District

Jody Ruckman

Missouri River Project Office, Omaha NE

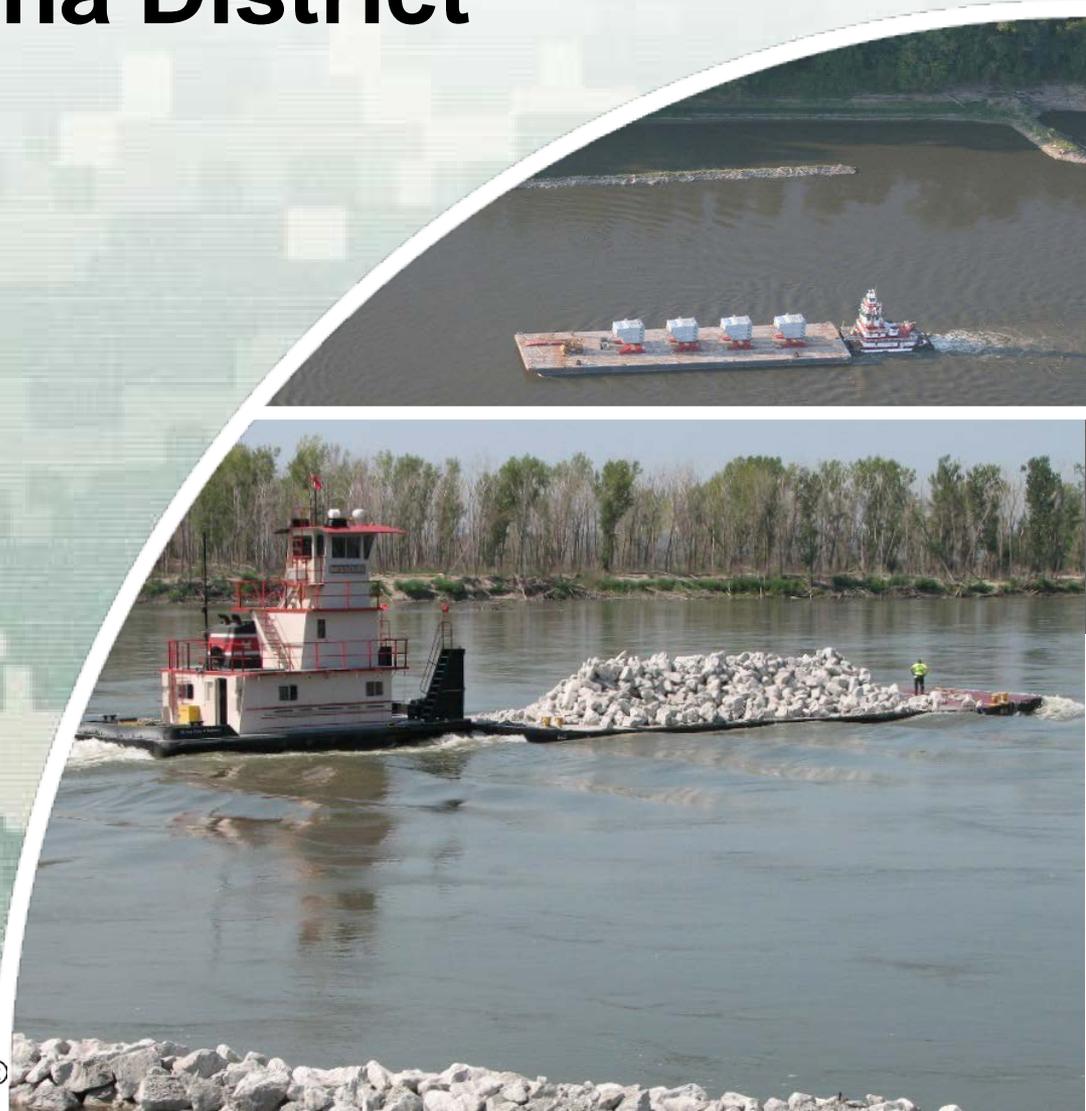

US Army Corps of Engineers
BUILDING STRONG[®]



[®]

Missouri River Project Maintenance - 2013



Work Boat/barge at Nishnabotna River, March 2013



Meeting the Challenge



Lower Decatur Bend, Nov. 2013



BUILDING STRONG®

Revetment Kicker Restoration above Blair, Nebraska



November 2013



BUILDING STRONG®

M/V Tigre, April 2013



Maintenance partner working the post-flood high priority contract repairs above Boyer Bend.



BUILDING STRONG®

Quarry at Fort Calhoun, Nebraska



June 2013



BUILDING STRONG®

M/V Allison Marie Pushing Out from Quarry




More contract work above Boyer Bend, June 2013.



BUILDING STRONG®

New Challenges

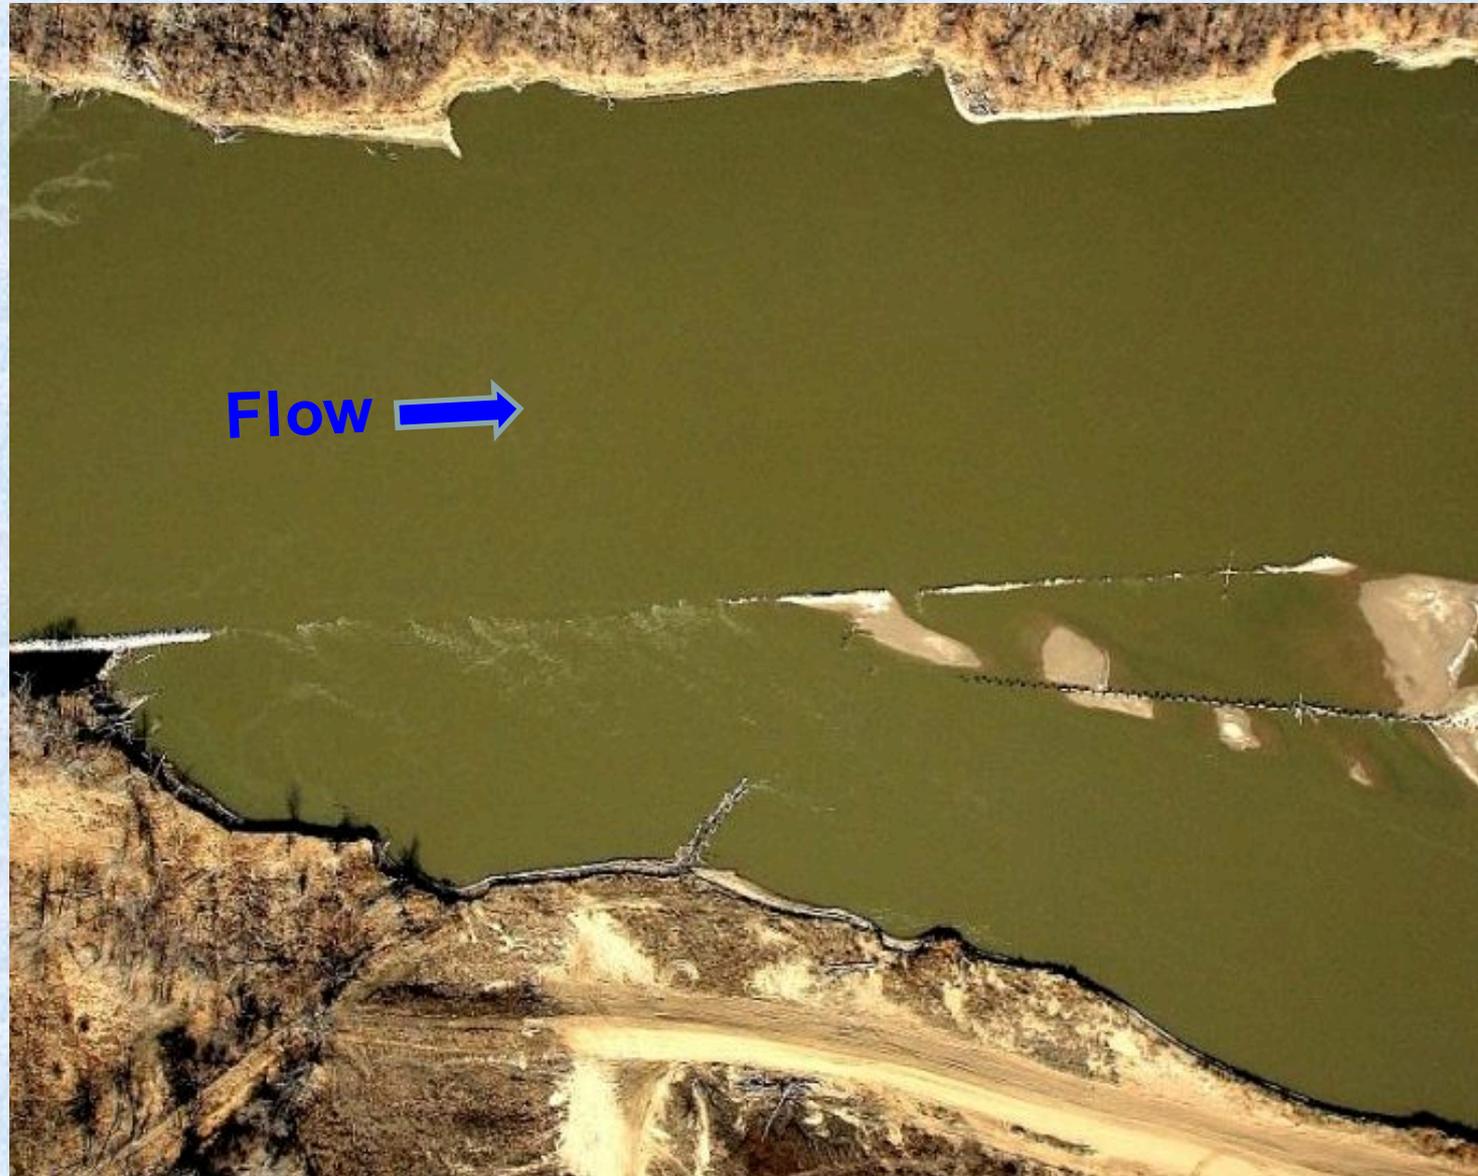

Flanked Dike Field, Upper Sonora Bend, March 2013



BUILDING STRONG®

M/V Expedition Upbound to Quarry



Upper Sonora Bend, July 2013



BUILDING STRONG®

M/V Mary Lynn at Nebraska City



April 2013



BUILDING STRONG®

DRAA Construction Summary13

- Upper / Lower Hamburg Closure BY Excavating (subbed to Western)
 - ▶ Total of Tons 15,000 Tons / 100% Complete
- BSNP North Phase 1 Newt Marine
 - ▶ Total of Tons 114,850 Tons / 100% Complete
- BSNP South Phase 1 Western
 - ▶ Total of Tons 135,850 Tons / 100 % Complete
- BSNP North Phase 2 Big River
 - ▶ Total of Tons 120,600 Tons / 20 % Complete
- BSNP South Phase 2 Big River
 - ▶ Total of Tons 145,000 Tons / 20% Complete



MRPO Budget Summary

- FY 10 \$1,400,514
- FY 11 \$1,433,000
- FY 12 \$1,988,849
- FY 13 \$1,752,917
- FY 14 \$1,881,937



Significant Channel Work Planned for 2014

- USACE

- ▶ 22 Mar investigate degradation of river bed and its potential effects on in channel historic structures.
- ▶ Remaining season may allow placement of only 20,000 tons of maintenance rock.

- By Contract

- ▶ Continuation of post-flood task order: Looking for placement of 95,000 tons in 2014.



Questions



BUILDING STRONG®
