

**Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006**

[illegible]

**GREEN - Secondary Document submit & review period**  
**RED - Primary Document submit & review period**

Split



## Milestone




## Project Summary



### External Milestone



Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

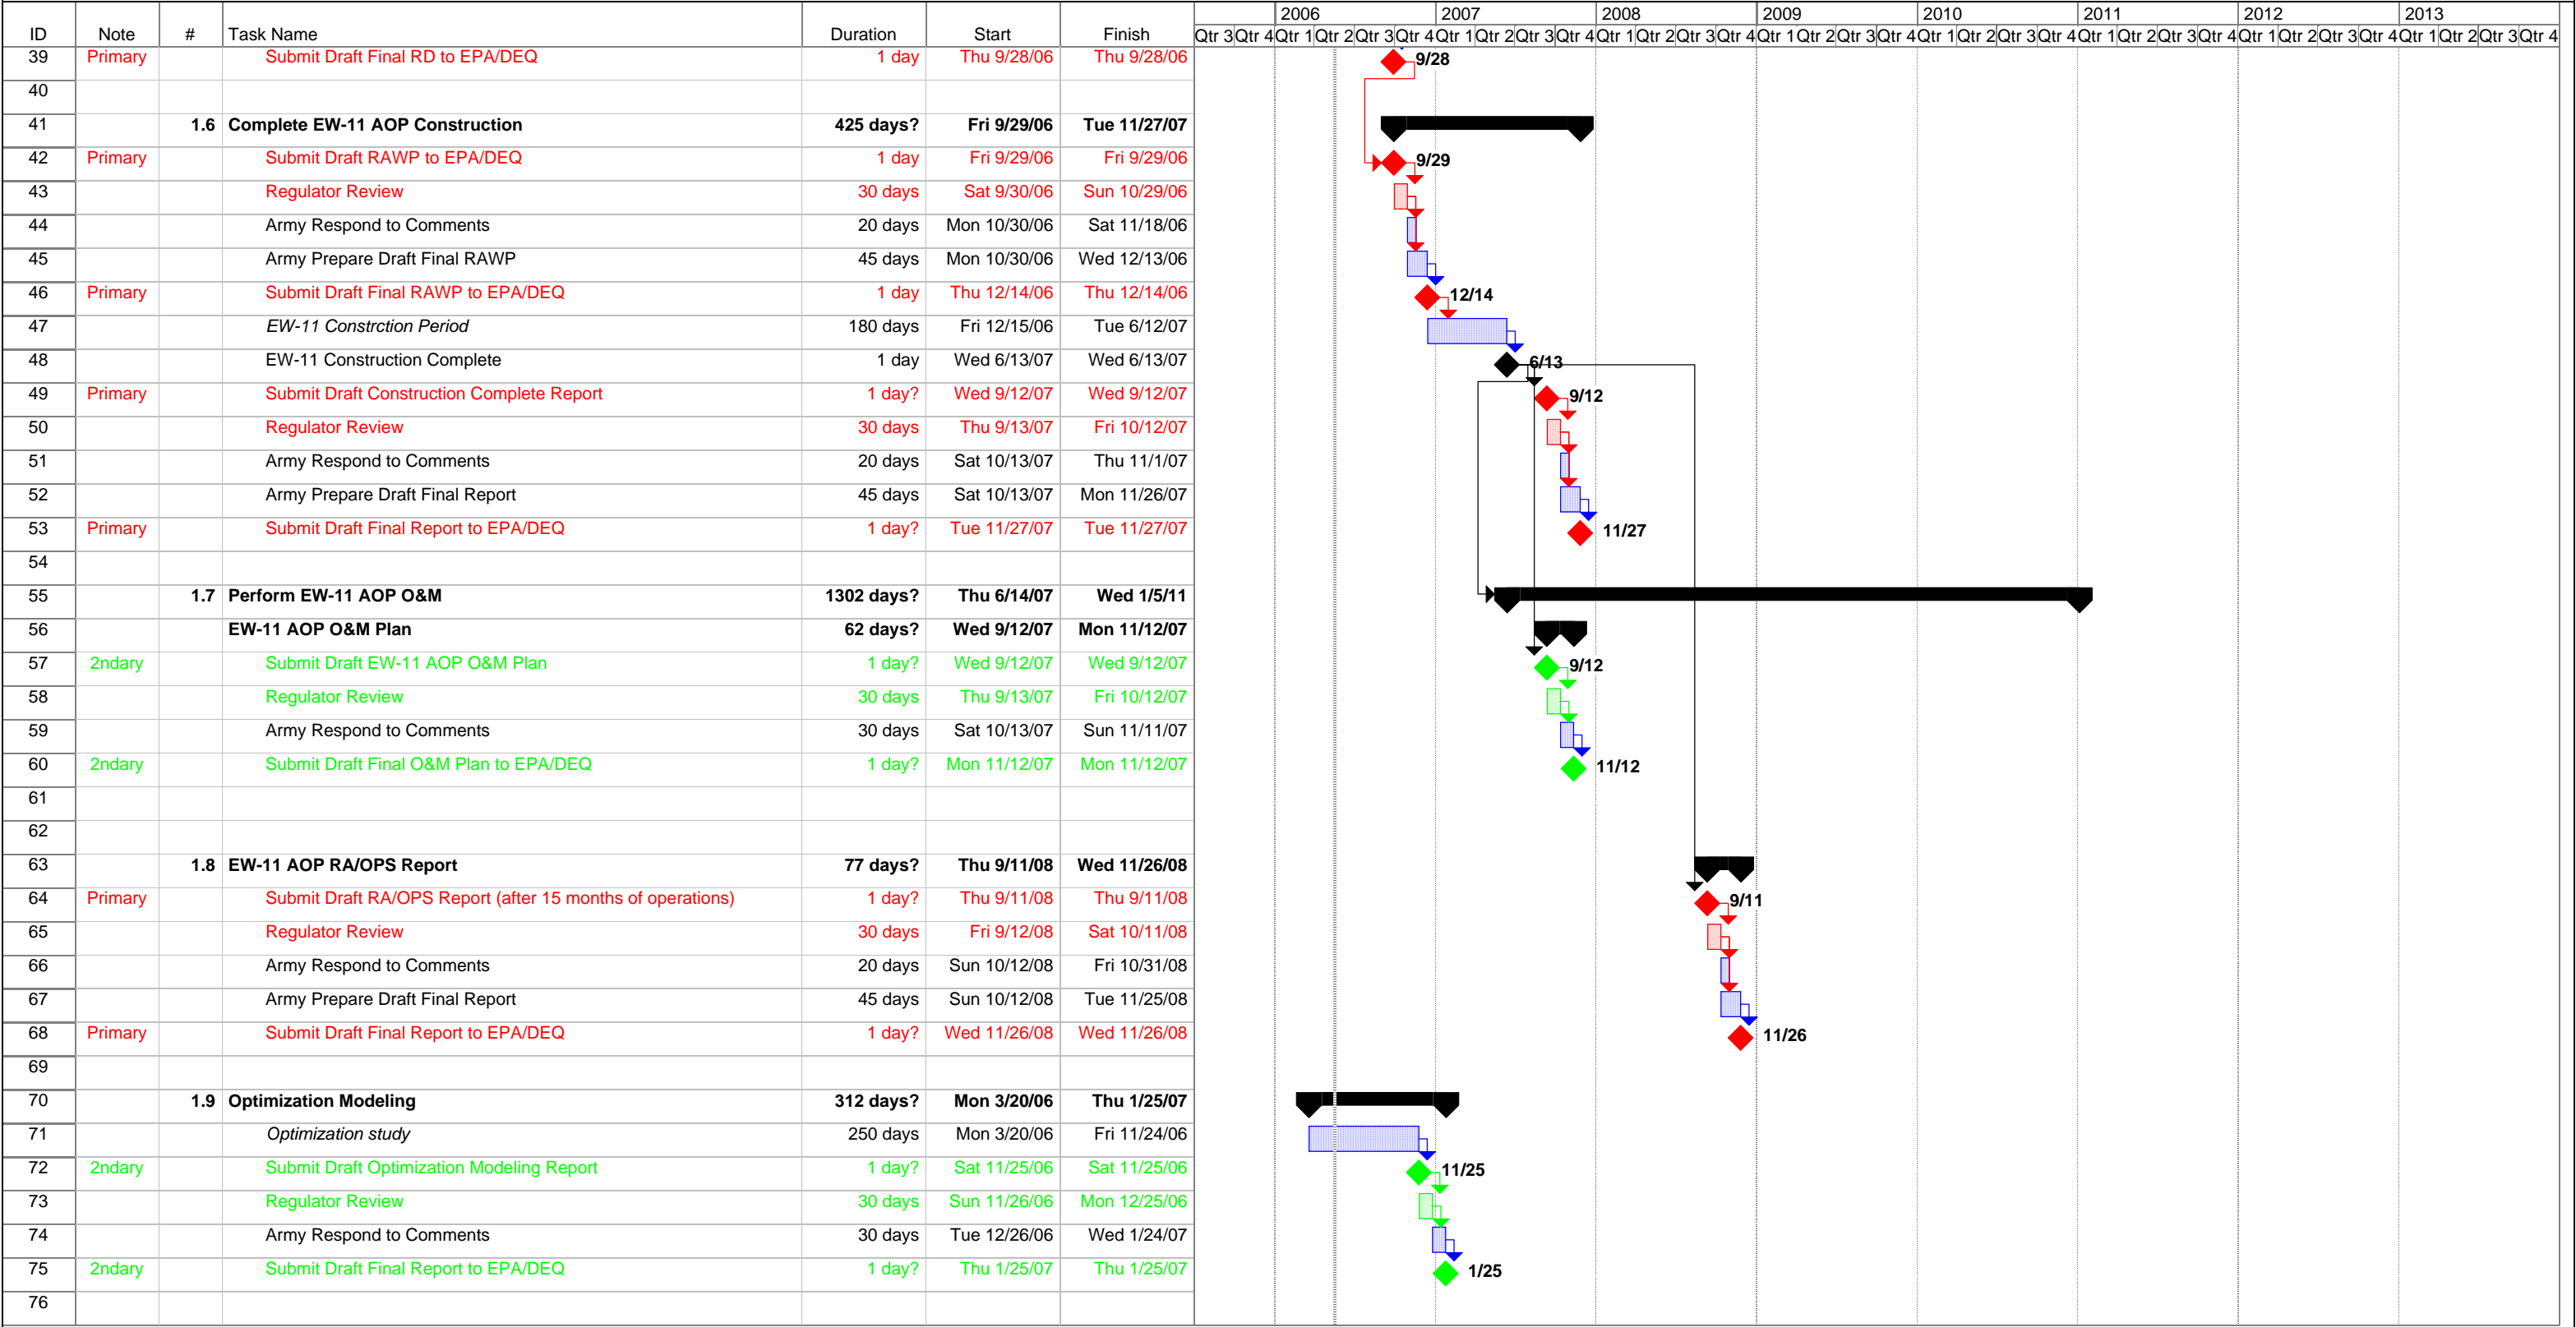

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task

Split

Progress

Milestone

Summary

Project Summary


External Tasks

External Milestone

Deadline


Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

ID	Note	#	Task Name	Duration	Start	Finish	2006				2007				2008				2009				2010				2011				2012				2013			
							Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		
77																																						
78																																						
79		2.0	Plume Interior Investigation & Focused Extraction	2533 days?	Fri 9/29/06	Wed 9/4/13																																
80		2.1	Complete GCW Technical Specifications	77 days?	Mon 1/29/07	Sun 4/15/07																																
81	Primary		Submit Draft RD to EPA/DEQ	1 day?	Mon 1/29/07	Mon 1/29/07																																
82			Regulator Review	30 days	Tue 1/30/07	Wed 2/28/07																																
83			Army Respond to Comments	20 days	Thu 3/1/07	Tue 3/20/07																																
84			Army Prepare Draft Final RD	45 days	Thu 3/1/07	Sat 4/14/07																																
85	Primary		Submit Draft Final RD	1 day?	Sun 4/15/07	Sun 4/15/07																																
86																																						
87		2.2	NOP Sector 4 (Eastern side - LL4)	1431 days?	Fri 9/29/06	Sun 8/29/10																																
88	Primary	2.2.1	Submit Draft Pre-Design Investigation WP	1 day?	Fri 9/29/06	Fri 9/29/06																																
89			Regulator Review	30 days	Sat 9/30/06	Sun 10/29/06																																
90			Army Respond to Comments	20 days	Mon 10/30/06	Sat 11/18/06																																
91			Army Prepare Draft Final WP	45 days	Mon 10/30/06	Wed 12/13/06																																
92	Primary		Submit Draft Final PDI WP to EPA/DEQ	1 day?	Thu 12/14/06	Thu 12/14/06																																
93																																						
94		2.2.2	Investigation Field Work	60 days	Mon 1/22/07	Thu 3/22/07																																
95																																						
96	Primary	2.2.3	Submit Draft PDI Report	1 day?	Tue 5/22/07	Tue 5/22/07																																
97			Regulator Review	30 days	Wed 5/23/07	Thu 6/21/07																																
98			Army Respond to Comments	20 days	Fri 6/22/07	Wed 7/11/07																																
99			Army Prepare Draft Final Report	45 days	Fri 6/22/07	Sun 8/5/07																																
100	Primary		Submit Draft Final PDI Report to EPA/DEQ	1 day?	Mon 8/6/07	Mon 8/6/07																																
101																																						
102	Primary	2.2.4	Submit Draft Technology Screening Report (mini-FS)	1 day?	Fri 9/21/07	Fri 9/21/07																																
103			Regulator Review	30 days	Sat 9/22/07	Sun 10/21/07																																
104			Army Respond to Comments	20 days	Mon 10/22/07	Sat 11/10/07																																
105			Army Prepare Draft Final Report	45 days	Sun 11/11/07	Tue 12/25/07																																
106	Primary		Submit Draft Final TS Report to EPA/DEQ	1 day?	Wed 12/26/07	Wed 12/26/07																																
107																																						
108	Primary	2.2.5	Submit Draft Remedial Design	1 day?	Sun 2/10/08	Sun 2/10/08																																
109			Regulator Review	30 days	Mon 2/11/08	Tue 3/11/08																																
110			Army Respond to Comments	20 days	Wed 3/12/08	Mon 3/31/08																																
111			Army Prepare Draft Final Report	45 days	Tue 4/1/08	Thu 5/15/08																																
112	Primary		Submit Draft Final RD to EPA/DEQ	1 day?	Fri 5/16/08	Fri 5/16/08																																
113																																						
114	Primary	2.2.6	Submit Draft RAWP (for GCW or other)	1 day?	Sat 5/17/08	Sat 5/17/08																																

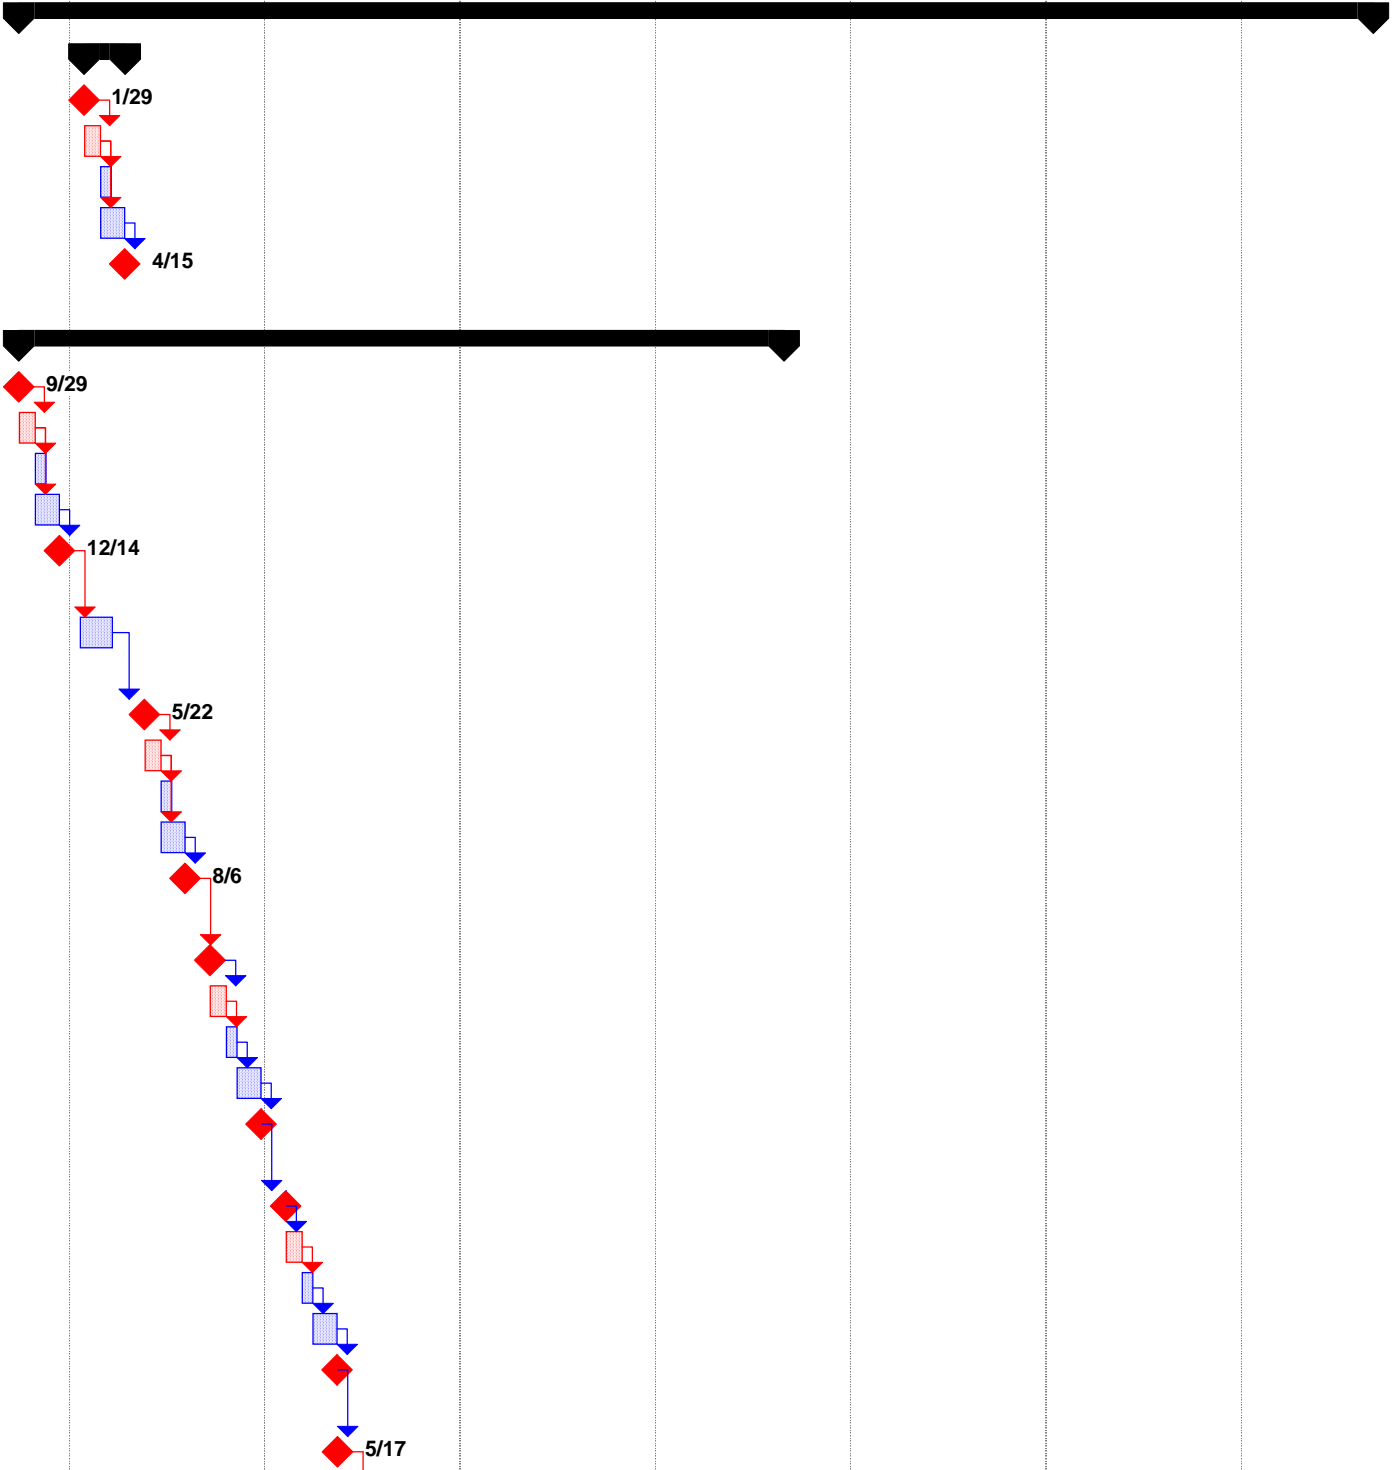

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task  
Split



Progress  
Milestone



Summary  
Project Summary




External Tasks  
External Milestone



Deadline



Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

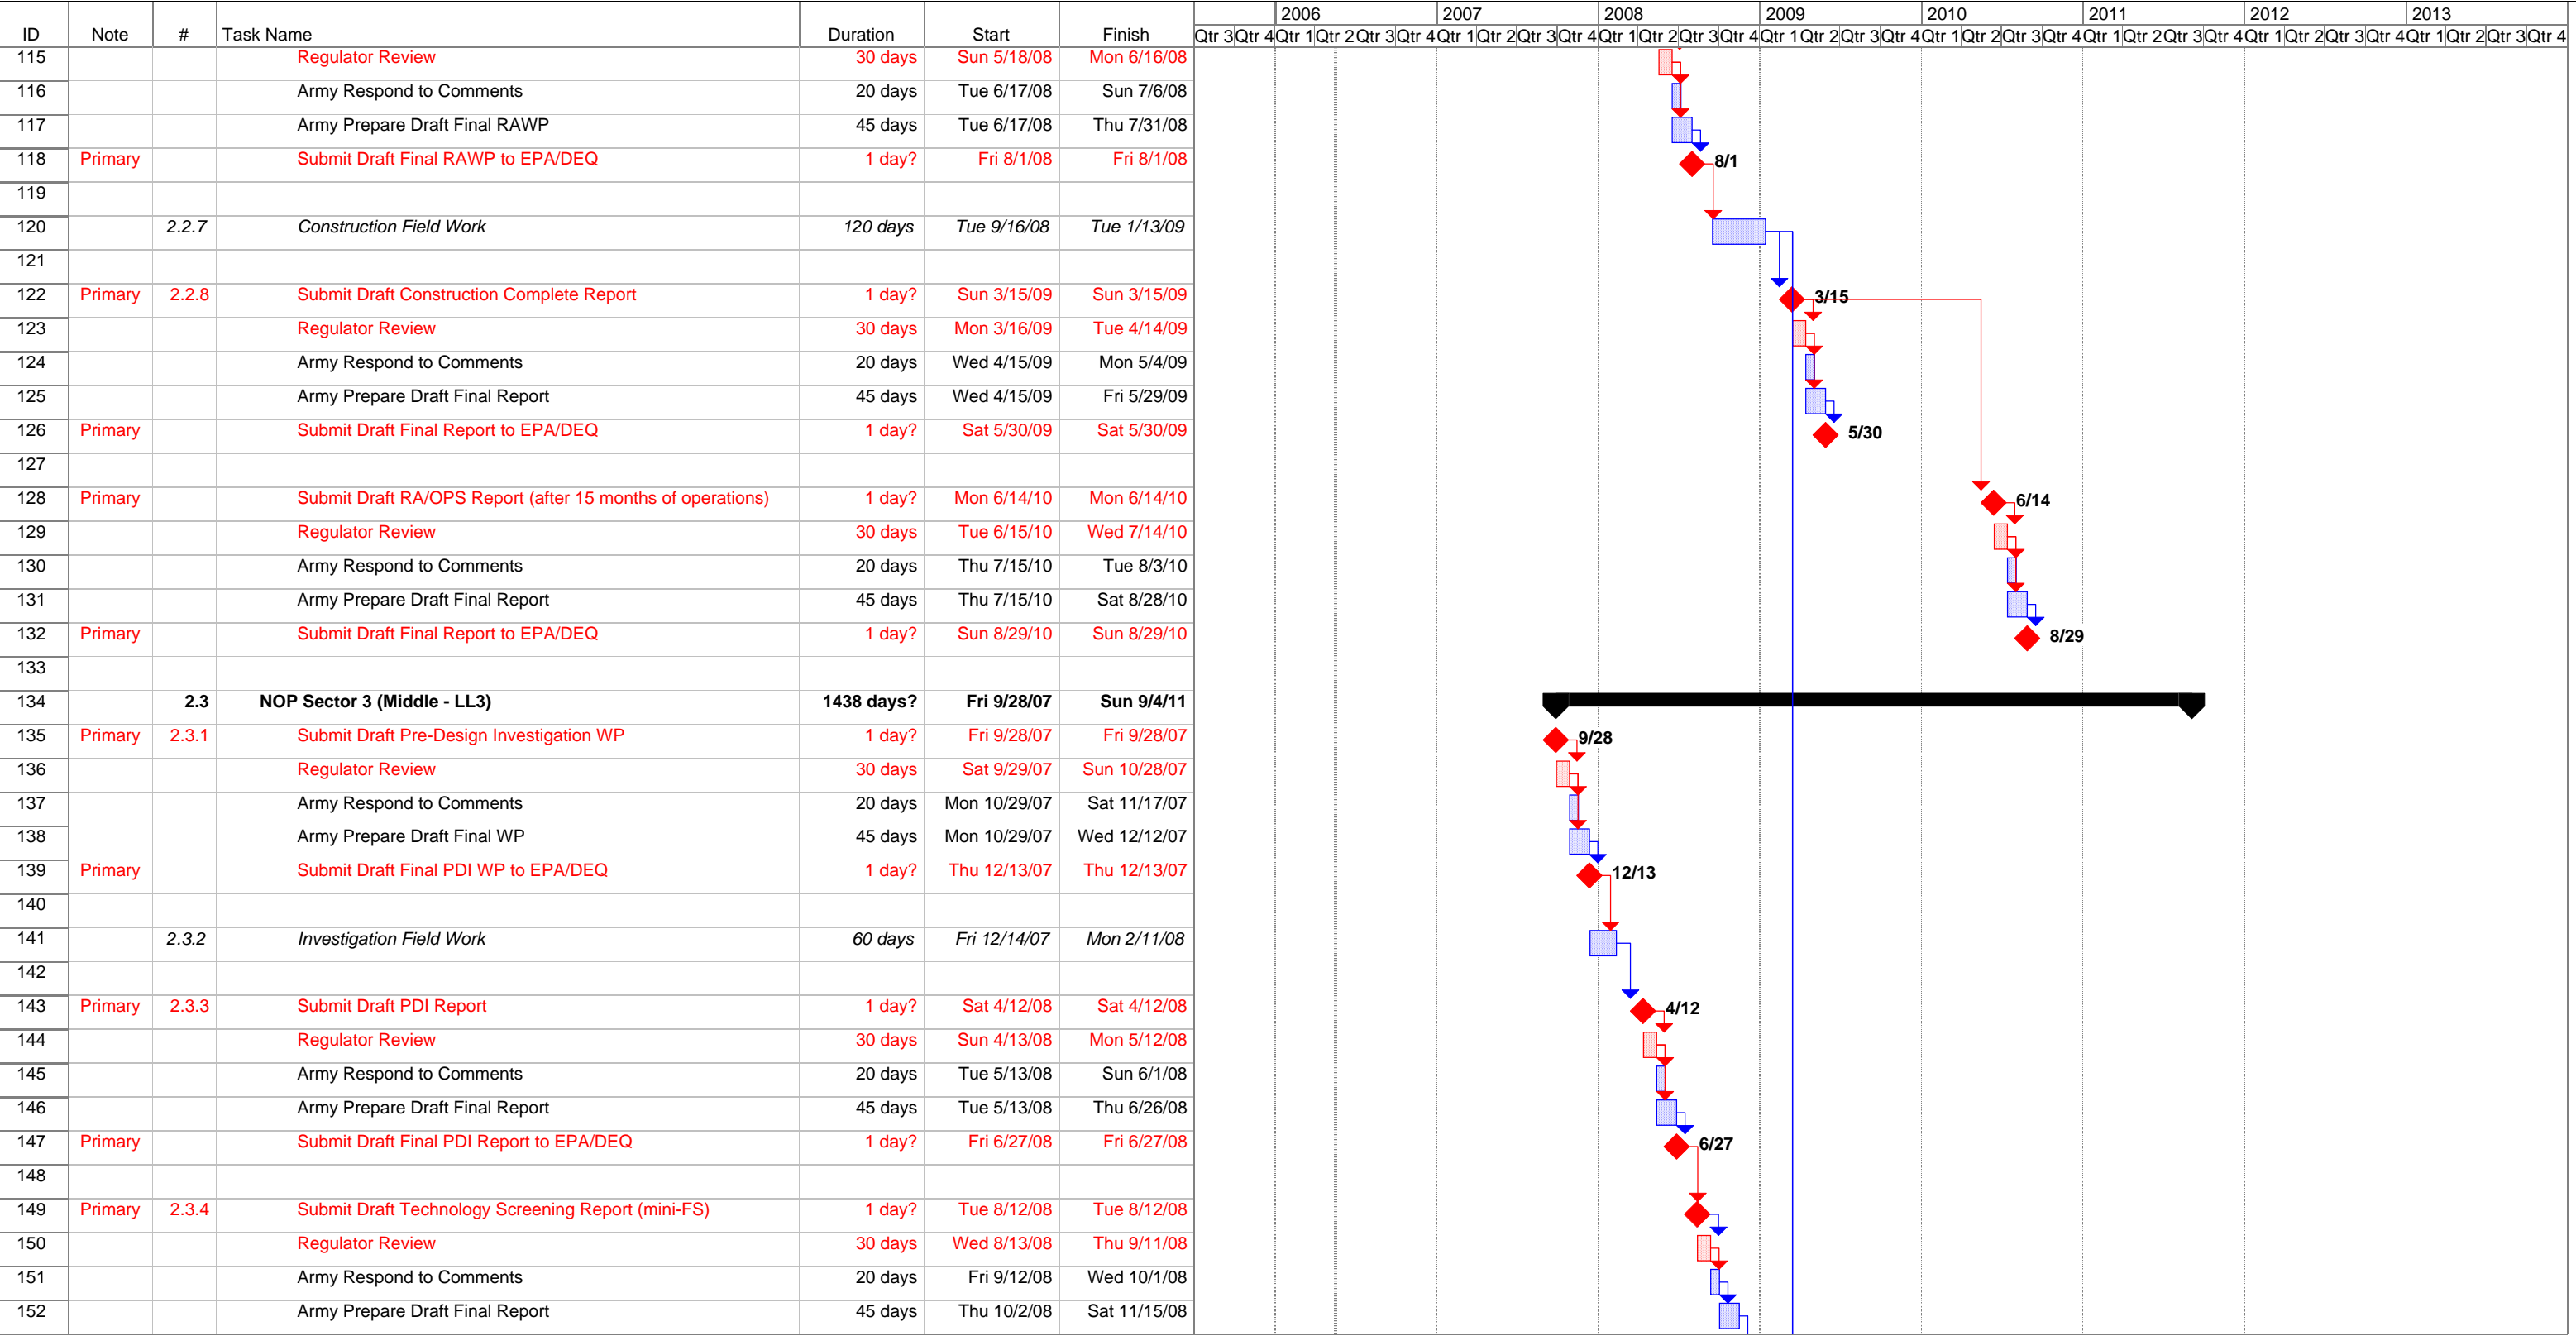

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline

**Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006**

ID	Note	#	Task Name	Duration	Start	Finish	2006				2007				2008				2009				2010				2011				2012				2013			
							Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		
153	Primary		Submit Draft Final TS Report to EPA/DEQ	1 day?	Sun 11/16/08	Sun 11/16/08																																
154																																						
155	Primary	2.2.5	Submit Draft Remedial Design	1 day?	Thu 1/1/09	Thu 1/1/09																																
156			Regulator Review	30 days	Fri 1/2/09	Sat 1/31/09																																
157			Army Respond to Comments	20 days	Sun 2/1/09	Fri 2/20/09																																
158			Army Prepare Draft Final Report	45 days	Sat 2/21/09	Mon 4/6/09																																
159	Primary		Submit Draft Final RD to EPA/DEQ	1 day?	Tue 4/7/09	Tue 4/7/09																																
160																																						
161	Primary	2.3.6	Submit Draft RAWP (for GCW or other)	1 day?	Sat 5/23/09	Sat 5/23/09																																
162			Regulator Review	30 days	Sun 5/24/09	Mon 6/22/09																																
163			Army Respond to Comments	20 days	Tue 6/23/09	Sun 7/12/09																																
164			Army Prepare Draft Final RAWP	45 days	Tue 6/23/09	Thu 8/6/09																																
165	Primary		Submit Draft Final RAWP to EPA/DEQ	1 day?	Fri 8/7/09	Fri 8/7/09																																
166																																						
167		2.3.7	Construction Field Work	120 days	Tue 9/22/09	Tue 1/19/10																																
168																																						
169	Primary	2.3.8	Submit Draft Construction Complete Report	1 day?	Sun 3/21/10	Sun 3/21/10																																
170			Regulator Review	30 days	Mon 3/22/10	Tue 4/20/10																																
171			Army Respond to Comments	20 days	Wed 4/21/10	Mon 5/10/10																																
172			Army Prepare Draft Final Report	45 days	Wed 4/21/10	Fri 6/4/10																																
173	Primary		Submit Draft Final Report to EPA/DEQ	1 day?	Sat 6/5/10	Sat 6/5/10																																
174																																						
175	Primary		Submit Draft RA/OPS Report (after 15 months of operations)	1 day?	Mon 6/20/11	Mon 6/20/11																																
176			Regulator Review	30 days	Tue 6/21/11	Wed 7/20/11																																
177			Army Respond to Comments	20 days	Thu 7/21/11	Tue 8/9/11																																
178			Army Prepare Draft Final Report	45 days	Thu 7/21/11	Sat 9/3/11																																
179	Primary		Submit Draft Final Report to EPA/DEQ	1 day?	Sun 9/4/11	Sun 9/4/11																																
180																																						
181		2.4	NOP Sector 2 (Middle - LL2)	1438 days?	Mon 9/29/08	Wed 9/5/12																																
182	Primary	2.4.1	Submit Draft Pre-Design Investigation WP	1 day?	Mon 9/29/08	Mon 9/29/08																																
183			Regulator Review	30 days	Tue 9/30/08	Wed 10/29/08																																
184			Army Respond to Comments	20 days	Thu 10/30/08	Tue 11/18/08																																
185			Army Prepare Draft Final WP	45 days	Thu 10/30/08	Sat 12/13/08																																
186	Primary		Submit Draft Final PDI WP to EPA/DEQ	1 day?	Sun 12/14/08	Sun 12/14/08																																
187																																						
188		2.4.2	Investigation Field Work	60 days	Mon 12/15/08	Thu 2/12/09																																
189																																						
190	Primary	2.4.3	Submit Draft PDI Report	1 day?	Tue 4/14/09	Tue 4/14/09																																

**GREEN - Secondary Document submit & review period**  
**RED - Primary Document submit & review period**


Split

## Milestone

## Project Summary

### External Milestone

Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

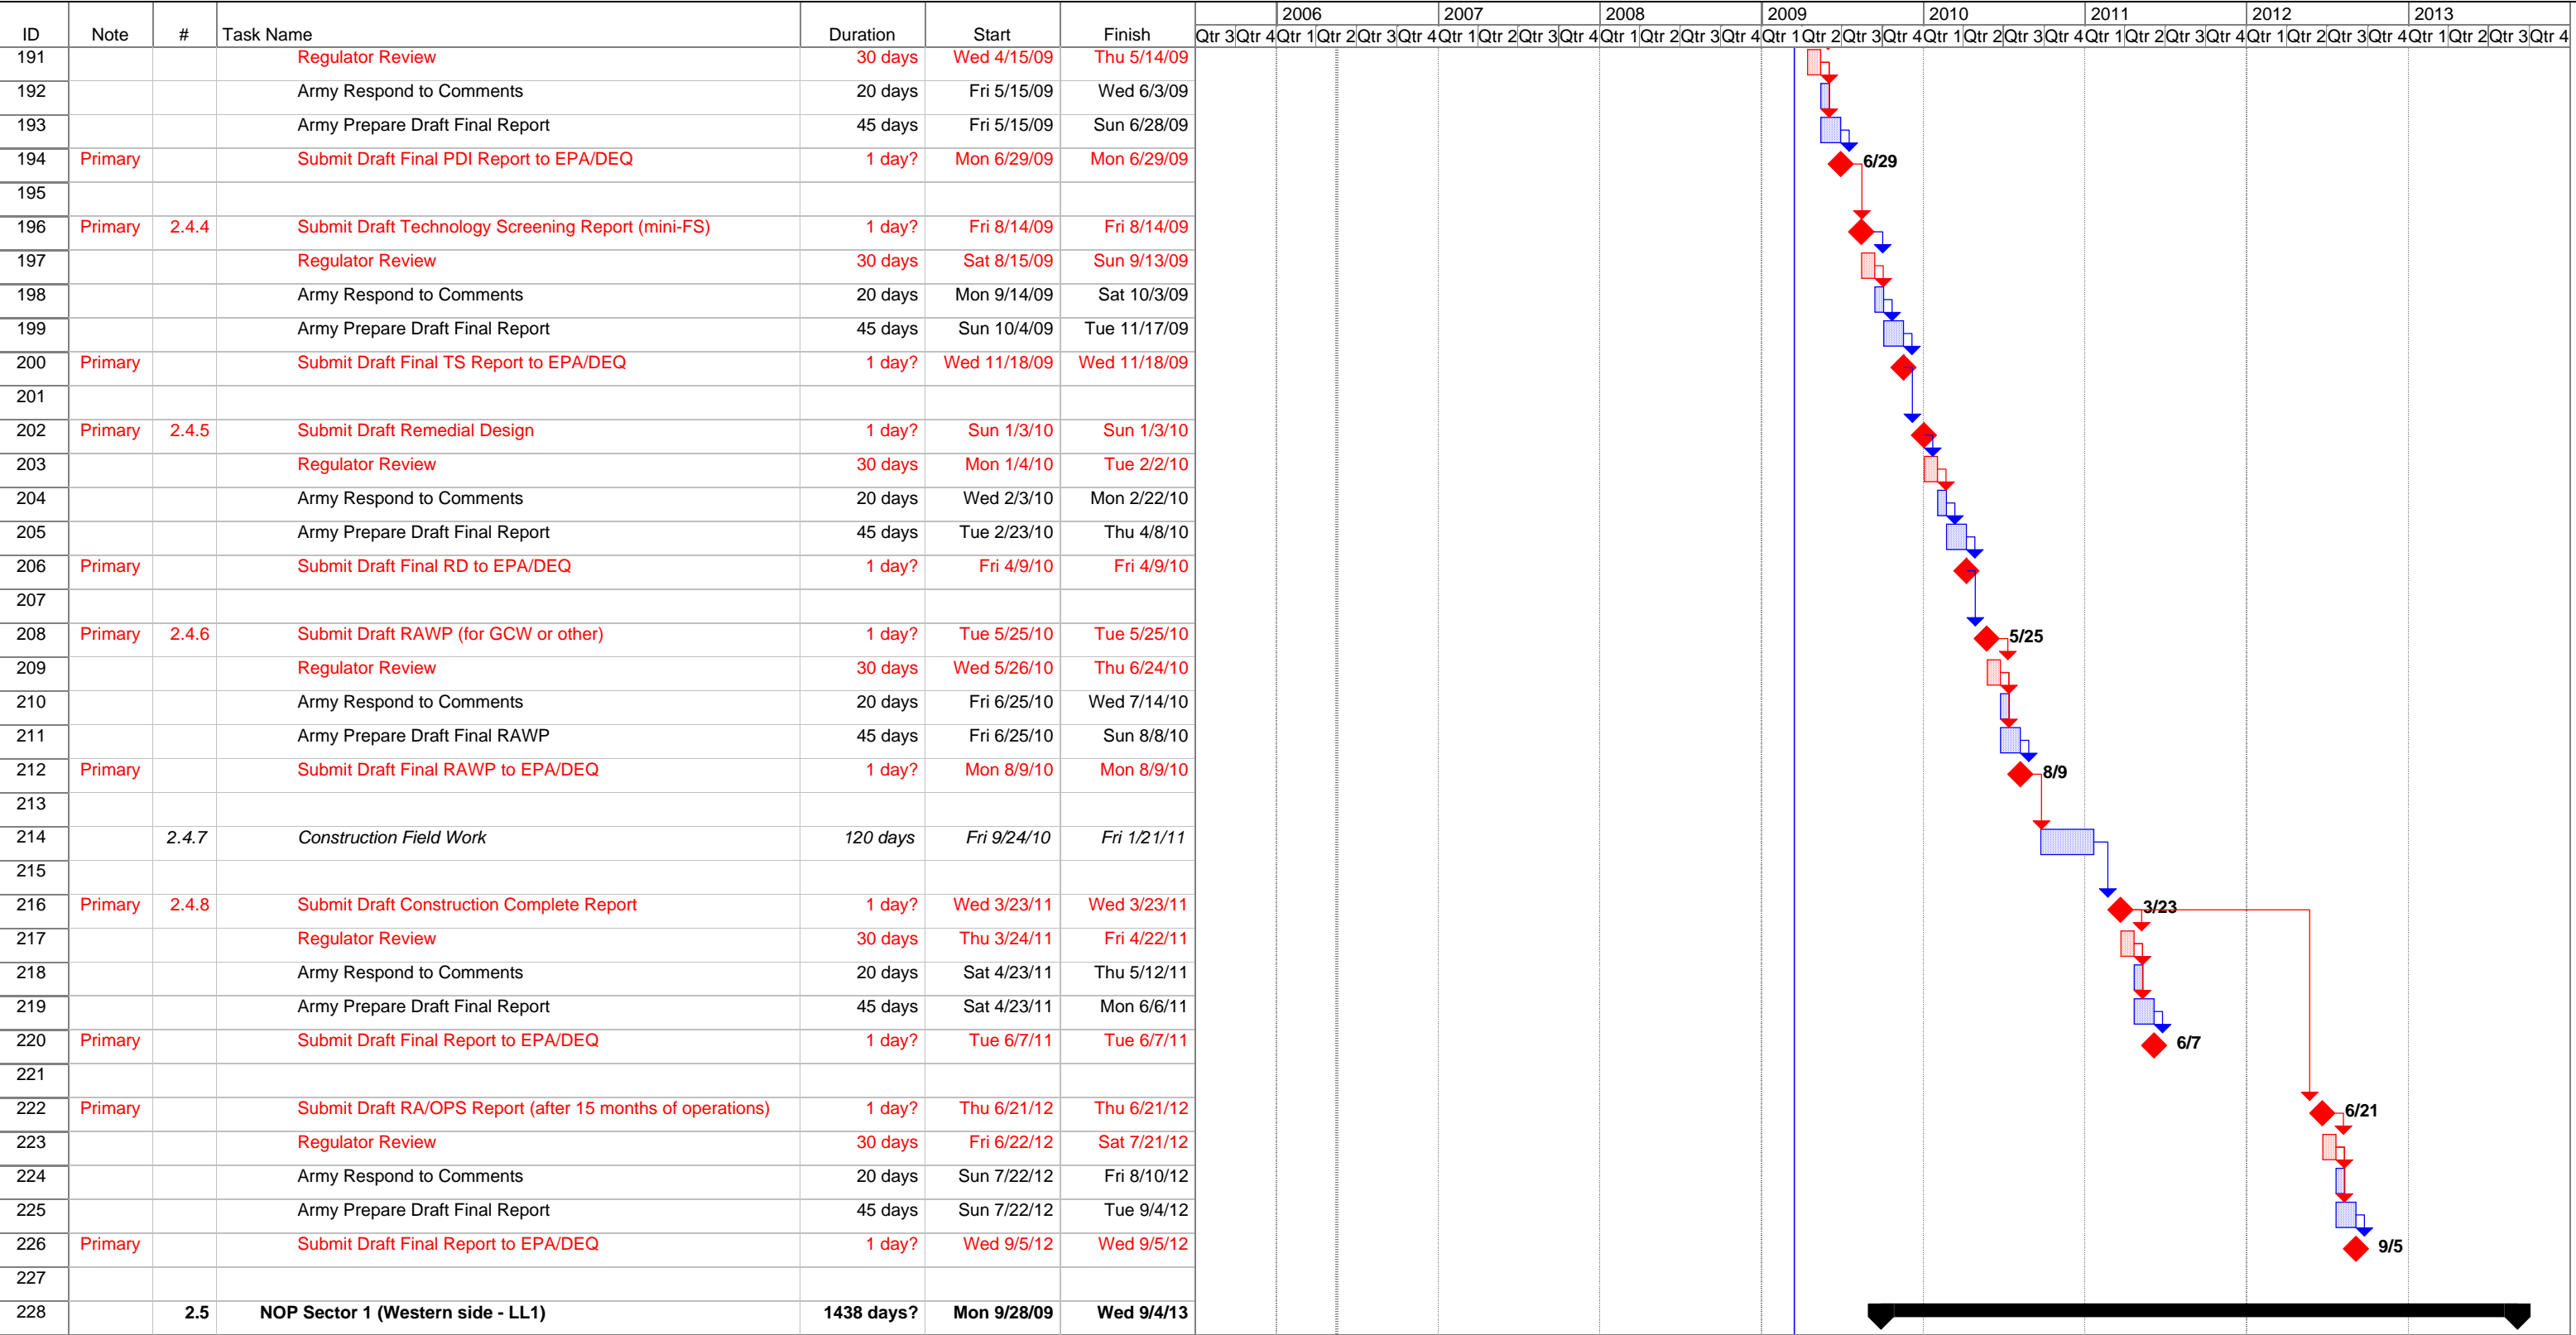

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline



**Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006**

ID	Note	#	Task Name	Duration	Start	Finish
229	Primary	2.5.1	Submit Draft Pre-Design Investigation WP	1 day?	Mon 9/28/09	Mon 9/28/09
230			Regulator Review	30 days	Tue 9/29/09	Wed 10/28/09
231			Army Respond to Comments	20 days	Thu 10/29/09	Tue 11/17/09
232			Army Prepare Draft Final WP	45 days	Thu 10/29/09	Sat 12/12/09
233	Primary		Submit Draft Final PDI WP to EPA/DEQ	1 day?	Sun 12/13/09	Sun 12/13/09
234						
235		2.5.2	Investigation Field Work	60 days	Mon 12/14/09	Thu 2/11/10
236						
237	Primary	2.5.3	Submit Draft PDI Report	1 day?	Tue 4/13/10	Tue 4/13/10
238			Regulator Review	30 days	Wed 4/14/10	Thu 5/13/10
239			Army Respond to Comments	20 days	Fri 5/14/10	Wed 6/2/10
240			Army Prepare Draft Final Report	45 days	Fri 5/14/10	Sun 6/27/10
241	Primary		Submit Draft Final PDI Report to EPA/DEQ	1 day?	Mon 6/28/10	Mon 6/28/10
242						
243	Primary	2.5.4	Submit Draft Technology Screening Report (mini-FS)	1 day?	Fri 8/13/10	Fri 8/13/10
244			Regulator Review	30 days	Sat 8/14/10	Sun 9/12/10
245			Army Respond to Comments	20 days	Mon 9/13/10	Sat 10/2/10
246			Army Prepare Draft Final Report	45 days	Sun 10/3/10	Tue 11/16/10
247	Primary		Submit Draft Final TS Report to EPA/DEQ	1 day?	Wed 11/17/10	Wed 11/17/10
248						
249	Primary	2.5.5	Submit Draft Remedial Design	1 day?	Sun 1/2/11	Sun 1/2/11
250			Regulator Review	30 days	Mon 1/3/11	Tue 2/1/11
251			Army Respond to Comments	20 days	Wed 2/2/11	Mon 2/21/11
252			Army Prepare Draft Final Report	45 days	Tue 2/22/11	Thu 4/7/11
253	Primary		Submit Draft Final RD to EPA/DEQ	1 day?	Fri 4/8/11	Fri 4/8/11
254						
255	Primary	2.5.6	Submit Draft RAWP (for GCW or other)	1 day?	Tue 5/24/11	Tue 5/24/11
256			Regulator Review	30 days	Wed 5/25/11	Thu 6/23/11
257			Army Respond to Comments	20 days	Fri 6/24/11	Wed 7/13/11
258			Army Prepare Draft Final RAWP	45 days	Fri 6/24/11	Sun 8/7/11
259	Primary		Submit Draft Final RAWP to EPA/DEQ	1 day?	Mon 8/8/11	Mon 8/8/11
260						
261		2.5.7	Construction Field Work	120 days	Fri 9/23/11	Fri 1/20/12
262						
263	Primary	2.5.8	Submit Draft Construction Complete Report	1 day?	Wed 3/21/12	Wed 3/21/12
264			Regulator Review	30 days	Thu 3/22/12	Fri 4/20/12
265			Army Respond to Comments	20 days	Sat 4/21/12	Thu 5/10/12
266			Army Prepare Draft Final Report	45 days	Sat 4/21/12	Mon 6/4/12

**GREEN - Secondary Document submit & review period**  
**RED - Primary Document submit & review period**

Split



## Milestone



## Project Summary



### External Milestone



**Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006**

ID	Note	#	Task Name	Duration	Start	Finish
267	Primary		Submit Draft Final Report to EPA/DEQ	1 day?	Tue 6/5/12	Tue 6/5/12
268						
269	Primary		Submit Draft RA/OPS Report (after 15 months of operations)	1 day?	Thu 6/20/13	Thu 6/20/13
270			Regulator Review	30 days	Fri 6/21/13	Sat 7/20/13
271			Army Respond to Comments	20 days	Sun 7/21/13	Fri 8/9/13
272			Army Prepare Draft Final Report	45 days	Sun 7/21/13	Tue 9/3/13
273	Primary		Submit Draft Final Report to EPA/DEQ	1 day?	Wed 9/4/13	Wed 9/4/13
274						
275						
276		2.6	GCW (or other) O&M	62 days?	Tue 4/14/09	Sun 6/14/09
277	2ndary		Submit Draft O&M Plan for GCW's (or other)	1 day?	Tue 4/14/09	Tue 4/14/09
278			Regulator Review	30 days	Wed 4/15/09	Thu 5/14/09
279			Army Respond to Comments	30 days	Fri 5/15/09	Sat 6/13/09
280	2ndary		Submit Draft Final O&M Plan to EPA/DEQ	1 day?	Sun 6/14/09	Sun 6/14/09
281						
282		2.7	Restoration Time Modeling	330 days?	Mon 8/21/06	Mon 7/16/07
283	2ndary		Submit Draft Restoration Time Modeling Study Report	1 day?	Tue 7/17/07	Tue 7/17/07
284			Regulator Review	30 days	Wed 7/18/07	Thu 8/16/07
285			Army Respond to Comments	30 days	Fri 8/17/07	Sat 9/15/07
286	2ndary		Submit Draft Final Report to EPA/DEQ	1 day?	Sun 9/16/07	Sun 9/16/07
287						
288						
289						
290						
291		3.0	Annual Groundwater Monitoring Program	1975 days?	Mon 1/16/06	Mon 6/13/11
292		3.1	Perform Annual GMP Sampling	1975 days?	Mon 1/16/06	Mon 6/13/11
293			2005 GMP	63 days?	Tue 5/30/06	Mon 7/31/06
294	2ndary		Submit Draft 2005 GMP Report	1 day?	Tue 5/30/06	Tue 5/30/06
295			Regulator Review	30 days	Wed 5/31/06	Thu 6/29/06
296			Army Respond to Comments	30 days	Fri 6/30/06	Sat 7/29/06
297	2ndary		Submit Draft Final 2005 GMP Report	1 day?	Sun 7/30/06	Sun 7/30/06
298	***		Submit Non-IAG report of findings for other Non-DoD compounds detected - Not Subject to EPA/DEQ Review	1 day?	Mon 7/31/06	Mon 7/31/06
299						
300			2006 GMP	516 days?	Mon 1/16/06	Fri 6/15/07
301	2ndary		Submit Draft 2006 GMP Sampling Plan	1 day?	Mon 1/16/06	Mon 1/16/06
302			Regulator Review	30 days	Tue 1/17/06	Wed 2/15/06
303			Army Respond to Comments	30 days	Thu 2/16/06	Fri 3/17/06

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task

Split

Progress

Milestone◆

Summary

Project Summary


External Tasks

External Milestone◆

Deadline↓



Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

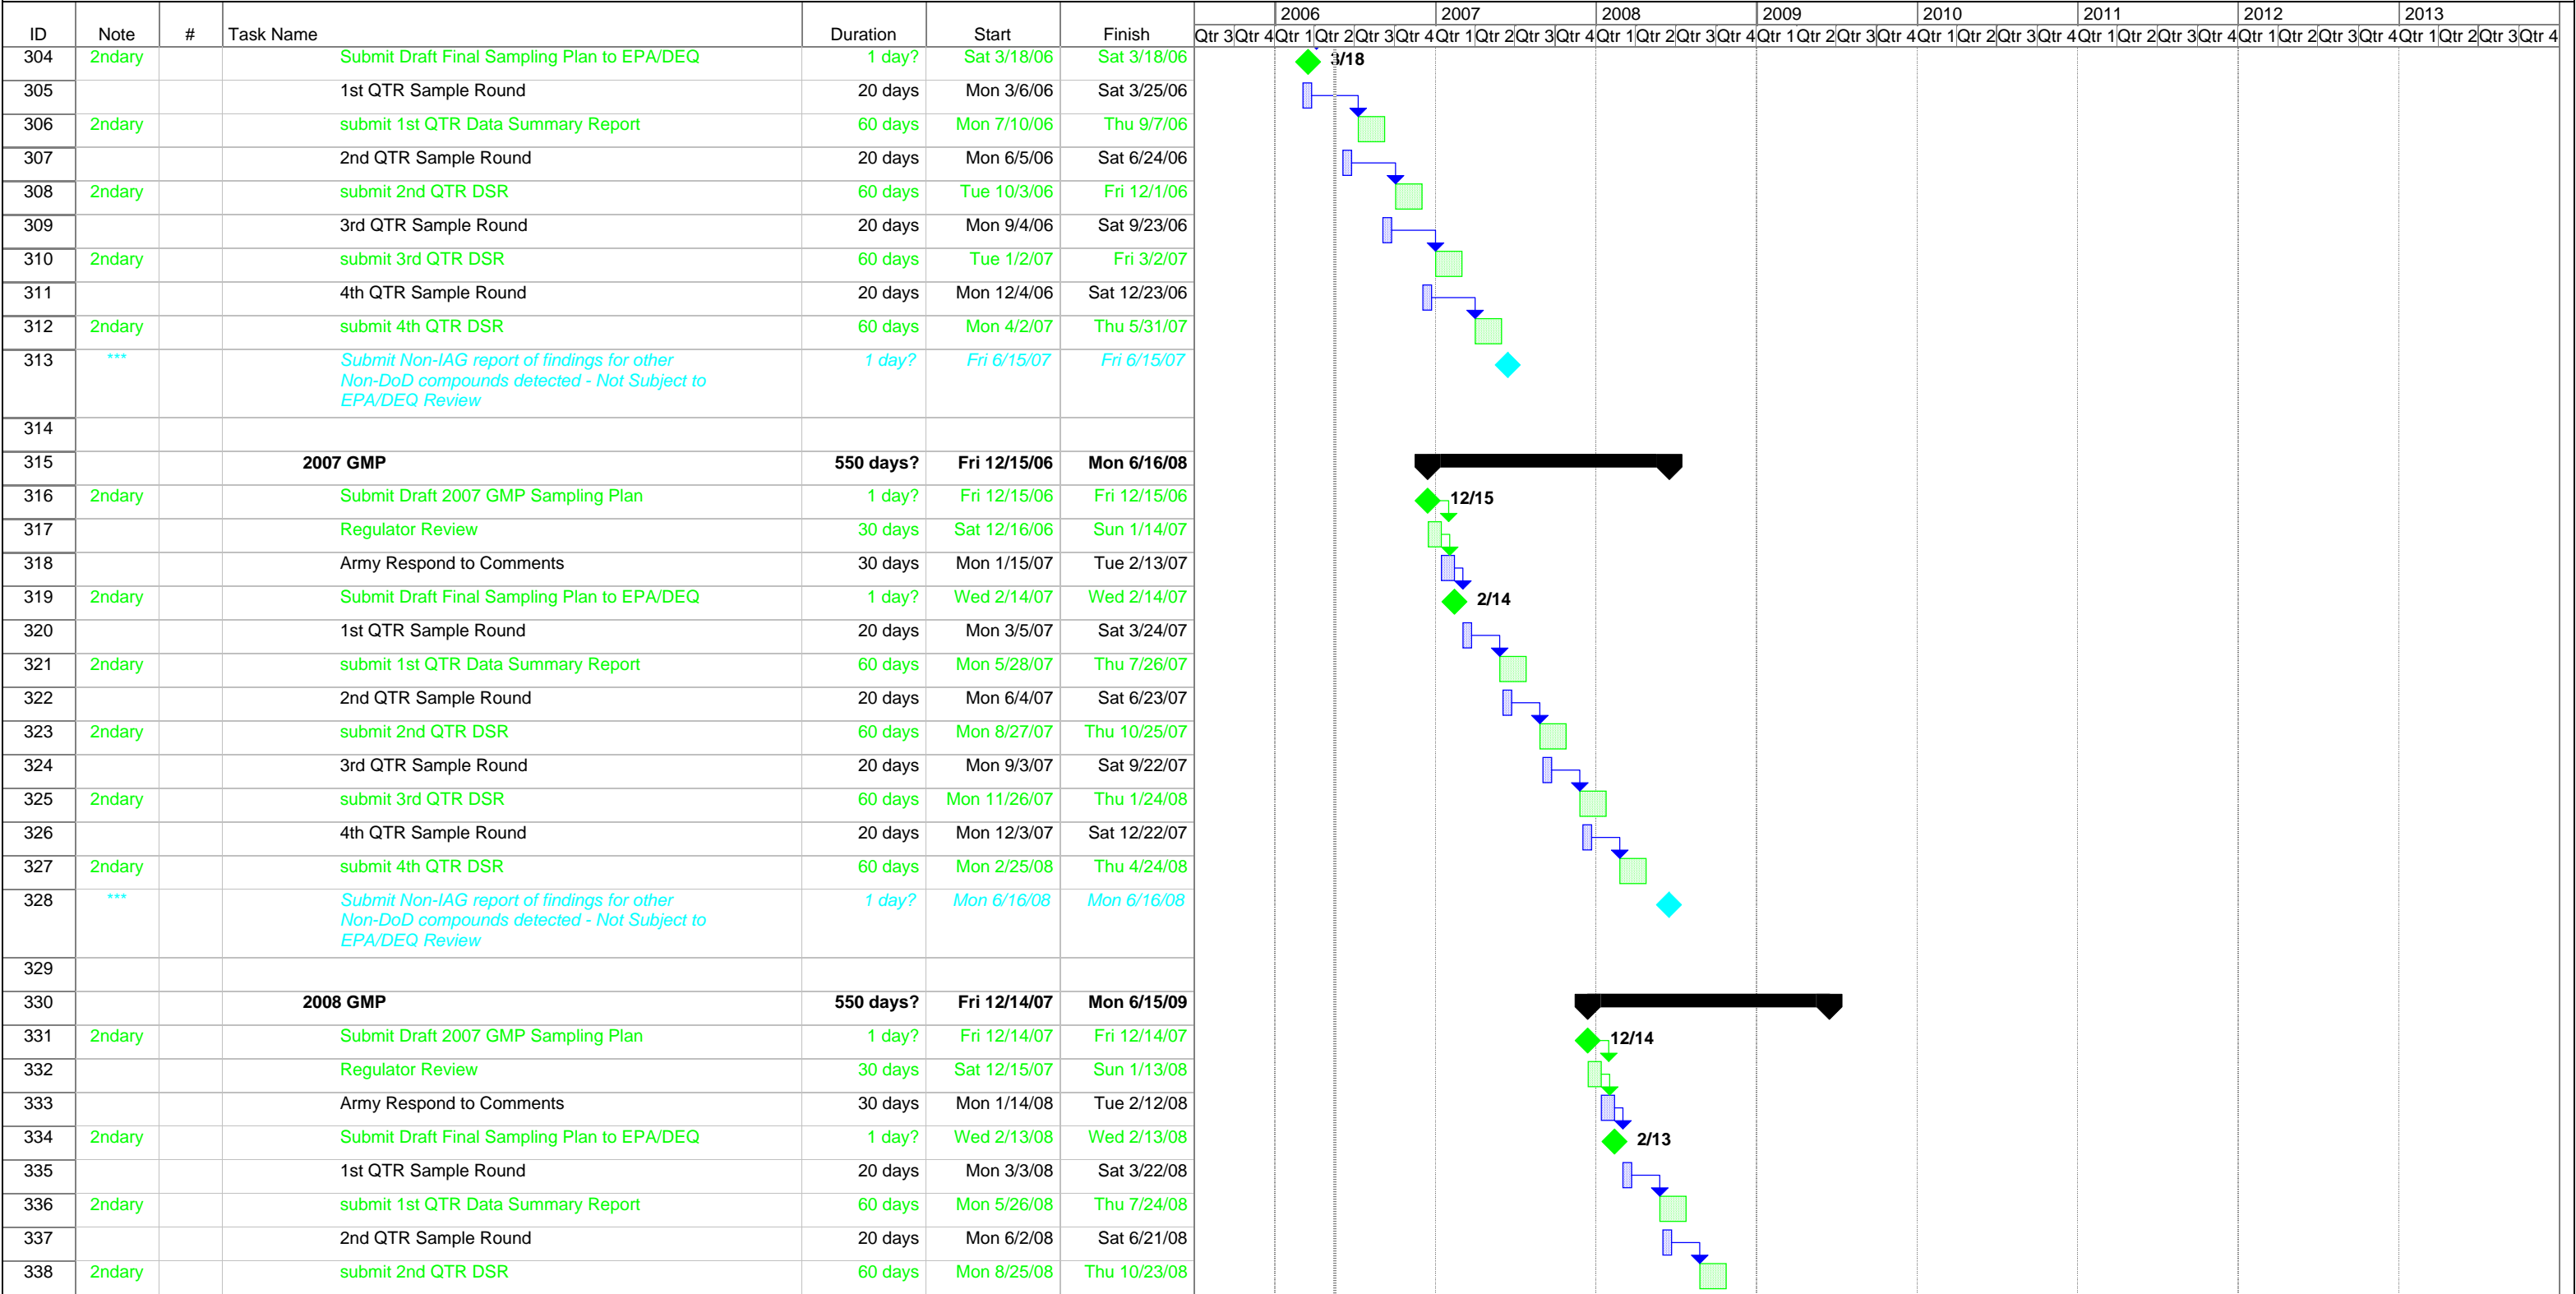

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline

**Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006**

ID	Note	#	Task Name	Duration	Start	Finish
339			3rd QTR Sample Round	20 days	Mon 9/1/08	Sat 9/20/08
340	2ndary		submit 3rd QTR DSR	60 days	Mon 11/24/08	Thu 1/22/09
341			4th QTR Sample Round	20 days	Mon 12/1/08	Sat 12/20/08
342	2ndary		submit 4th QTR DSR	60 days	Mon 2/23/09	Thu 4/23/09
343	***		Submit Non-IAG report of findings for other Non-DoD compounds detected - Not Subject to EPA/DEQ Review	1 day?	Mon 6/15/09	Mon 6/15/09
344						
345			2009 GMP	543 days?	Fri 12/19/08	Mon 6/14/10
346	2ndary		Submit Draft 2007 GMP Sampling Plan	1 day?	Fri 12/19/08	Fri 12/19/08
347			Regulator Review	30 days	Sat 12/20/08	Sun 1/18/09
348			Army Respond to Comments	30 days	Mon 1/19/09	Tue 2/17/09
349	2ndary		Submit Draft Final Sampling Plan to EPA/DEQ	1 day?	Wed 2/18/09	Wed 2/18/09
350			1st QTR Sample Round	20 days	Mon 3/2/09	Sat 3/21/09
351	2ndary		submit 1st QTR Data Summary Report	60 days	Mon 5/25/09	Thu 7/23/09
352			2nd QTR Sample Round	20 days	Mon 6/1/09	Sat 6/20/09
353	2ndary		submit 2nd QTR DSR	60 days	Mon 8/24/09	Thu 10/22/09
354			3rd QTR Sample Round	20 days	Mon 9/7/09	Sat 9/26/09
355	2ndary		submit 3rd QTR DSR	60 days	Mon 11/30/09	Thu 1/28/10
356			4th QTR Sample Round	20 days	Mon 12/7/09	Sat 12/26/09
357	2ndary		submit 4th QTR DSR	60 days	Fri 2/26/10	Mon 4/26/10
358	***		Submit Non-IAG report of findings for other Non-DoD compounds detected - Not Subject to EPA/DEQ Review	1 day?	Mon 6/14/10	Mon 6/14/10
359						
360			2010 GMP	543 days?	Fri 12/18/09	Mon 6/13/11
361	2ndary		Submit Draft 2007 GMP Sampling Plan	1 day?	Fri 12/18/09	Fri 12/18/09
362			Regulator Review	30 days	Sat 12/19/09	Sun 1/17/10
363			Army Respond to Comments	30 days	Mon 1/18/10	Tue 2/16/10
364	2ndary		Submit Draft Final Sampling Plan to EPA/DEQ	1 day?	Wed 2/17/10	Wed 2/17/10
365			1st QTR Sample Round	20 days	Mon 3/1/10	Sat 3/20/10
366	2ndary		submit 1st QTR Data Summary Report	60 days	Mon 5/24/10	Thu 7/22/10
367			2nd QTR Sample Round	20 days	Mon 6/7/10	Sat 6/26/10
368	2ndary		submit 2nd QTR DSR	60 days	Mon 8/30/10	Thu 10/28/10
369			3rd QTR Sample Round	20 days	Mon 9/6/10	Sat 9/25/10
370	2ndary		submit 3rd QTR DSR	60 days	Mon 11/29/10	Thu 1/27/11
371			4th QTR Sample Round	20 days	Mon 12/6/10	Sat 12/25/10
372	2ndary		submit 4th QTR DSR	60 days	Mon 2/28/11	Thu 4/28/11

**GREEN - Secondary Document submit & review period**  
**RED - Primary Document submit & review period**

Split

## Milestone

## Project Summary

### External Milestone

Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

ID	Note	#	Task Name	Duration	Start	Finish	2006				2007				2008				2009				2010				2011				2012				2013			
							Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		
373	***		Submit Non-IAG report of findings for other Non-DoD compounds detected - Not Subject to EPA/DEQ Review	1 day?	Mon 6/13/11	Mon 6/13/11																																
374																																						
375																																						
376		4.0	Annual Performance Evaluation	1649 days?	Wed 3/8/06	Sat 9/11/10																																
377		4.1	Complete Containment Evaluation Workplan	102 days?	Wed 3/8/06	Sat 6/17/06																																
378	Primary		Submit Draft WP to EPA/DEQ	1 day?	Wed 3/8/06	Wed 3/8/06																																
379			Regulator Review	40 days	Thu 3/9/06	Mon 4/17/06																																
380			Army Respond to Comments	32 days	Tue 4/18/06	Fri 5/19/06																																
381			Army Prepare Draft Final WP	60 days	Tue 4/18/06	Fri 6/16/06																																
382	Primary		Submit Draft Final WP to EPA/DEQ	1 day?	Sat 6/17/06	Sat 6/17/06																																
383																																						
384		4.2	Complete Periodic Model Updates	1469 days?	Mon 9/4/06	Sat 9/11/10																																
385	2ndary		Submit Draft 2006 Model Report to EPA/DEQ	1 day?	Mon 9/4/06	Mon 9/4/06																																
386			Regulator Review	30 days	Tue 9/5/06	Wed 10/4/06																																
387			Army Respond to Comments	30 days	Thu 10/5/06	Fri 11/3/06																																
388			Army Prepare Draft Final Report	30 days	Thu 10/5/06	Fri 11/3/06																																
389	2ndary		Submit Draft Final 2006 Model Report to EPA/DEQ	1 day?	Sat 11/4/06	Sat 11/4/06																																
390																																						
391	2ndary		Submit Draft 2008 Model Report to EPA/DEQ	1 day?	Mon 7/14/08	Mon 7/14/08																																
392			Regulator Review	30 days	Tue 7/15/08	Wed 8/13/08																																
393			Army Respond to Comments	30 days	Thu 8/14/08	Fri 9/12/08																																
394			Army Prepare Draft Final Report	30 days	Thu 8/14/08	Fri 9/12/08																																
395	2ndary		Submit Draft Final 2008 Model Report to EPA/DEQ	1 day?	Sat 9/13/08	Sat 9/13/08																																
396																																						
397	2ndary		Submit Draft 2010 Model Report to EPA/DEQ	1 day?	Mon 7/12/10	Mon 7/12/10																																
398			Regulator Review	30 days	Tue 7/13/10	Wed 8/11/10																																
399			Army Respond to Comments	30 days	Thu 8/12/10	Fri 9/10/10																																
400			Army Prepare Draft Final Report	30 days	Thu 8/12/10	Fri 9/10/10																																
401	2ndary		Submit Draft Final 2010 Model Report to EPA/DEQ	1 day?	Sat 9/11/10	Sat 9/11/10																																
402																																						
403		4.3	Complete Installation of new MW's & OW's for Containment	182 days?	Fri 6/30/06	Thu 12/28/06																																
404	Primary		Submit Well Installation WP	1 day?	Fri 6/30/06	Fri 6/30/06																																
405			Regulator Review	30 days	Sat 7/1/06	Sun 7/30/06																																
406			Army Respond to Comments	30 days	Mon 7/31/06	Tue 8/29/06																																
407			Army Prepare Draft Final Report	30 days	Mon 7/31/06	Tue 8/29/06																																
408	Primary		Submit Draft Final WP to EPA/DEQ	1 day?	Wed 8/30/06	Wed 8/30/06																																
409			Well Drilling	120 days	Thu 8/31/06	Thu 12/28/06																																

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task




Progress



Summary



External Tasks



Deadline



Split



Milestone



Project Summary



External Milestone



Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

ID	Note	#	Task Name	Duration	Start	Finish	2006				2007				2008				2009				2010				2011				2012				2013			
							Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		
410																																						
411		4.4	Complete Annual Remedy Performance Reports	1176 days?	Fri 7/20/07	Thu 10/7/10																																
412			2006 ARPR	77 days?	Fri 7/20/07	Thu 10/4/07																																
413	Primary		Submit Draft 2006 ARPR	1 day?	Fri 7/20/07	Fri 7/20/07																																
414			Regulator Review	30 days	Sat 7/21/07	Sun 8/19/07																																
415			Army Respond to Comments	20 days	Mon 8/20/07	Sat 9/8/07																																
416			Army Prepare Draft Final ARPR	45 days	Mon 8/20/07	Wed 10/3/07																																
417	Primary		Submit Draft Final ARPR to EPA/DEQ	1 day?	Thu 10/4/07	Thu 10/4/07																																
418																																						
419			2007 ARPR	77 days?	Fri 7/18/08	Thu 10/2/08																																
420	Primary		Submit Draft 2007 ARPR	1 day?	Fri 7/18/08	Fri 7/18/08																																
421			Regulator Review	30 days	Sat 7/19/08	Sun 8/17/08																																
422			Army Respond to Comments	20 days	Mon 8/18/08	Sat 9/6/08																																
423			Army Prepare Draft Final ARPR	45 days	Mon 8/18/08	Wed 10/1/08																																
424	Primary		Submit Draft Final ARPR to EPA/DEQ	1 day?	Thu 10/2/08	Thu 10/2/08																																
425																																						
426			2008 ARPR	77 days?	Fri 7/24/09	Thu 10/8/09																																
427	Primary		Submit Draft 2008 ARPR	1 day?	Fri 7/24/09	Fri 7/24/09																																
428			Regulator Review	30 days	Sat 7/25/09	Sun 8/23/09																																
429			Army Respond to Comments	20 days	Mon 8/24/09	Sat 9/12/09																																
430			Army Prepare Draft Final ARPR	45 days	Mon 8/24/09	Wed 10/7/09																																
431	Primary		Submit Draft Final ARPR to EPA/DEQ	1 day?	Thu 10/8/09	Thu 10/8/09																																
432																																						
433			2009 ARPR	77 days?	Fri 7/23/10	Thu 10/7/10																																
434	Primary		Submit Draft 2009 ARPR	1 day?	Fri 7/23/10	Fri 7/23/10																																
435			Regulator Review	30 days	Sat 7/24/10	Sun 8/22/10																																
436			Army Respond to Comments	20 days	Mon 8/23/10	Sat 9/11/10																																
437			Army Prepare Draft Final ARPR	45 days	Mon 8/23/10	Wed 10/6/10																																
438	Primary		Submit Draft Final ARPR to EPA/DEQ	1 day?	Thu 10/7/10	Thu 10/7/10																																
439																																						
440																																						
441		5.0	Eastern Plume Boundary Baseline & Monitoring	372 days?	Wed 2/22/06	Wed 2/28/07																																
442		5.1	Perform Eastern Perimeter Baseline Investigation	229 days?	Wed 2/22/06	Sun 10/8/06																																
443	Primary		Submit Phase 2 WP	1 day?	Wed 2/22/06	Wed 2/22/06																																
444			Regulator Review	7 days	Thu 2/23/06	Wed 3/1/06																																
445			Army Respond to Comments	7 days	Thu 3/2/06	Wed 3/8/06																																
446			Army Prepare Draft Final WP	7 days	Thu 3/2/06	Wed 3/8/06																																
447	Primary		Submit Draft Final WP to EPA/DEQ	1 day?	Thu 3/9/06	Thu 3/9/06																																

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task




Progress



Summary



External Tasks



Deadline



Split



Milestone



Project Summary



External Milestone



**Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006**

ID	Note	#	Task Name	Duration	Start	Finish	2006				2007				2008				2009				2010				2011				2012				2013					
							Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
448			Perform Field Work	30 days	Fri 3/10/06	Sat 4/8/06																																		
449	Primary		Submit Phase 2 Report	1 day?	Mon 7/24/06	Mon 7/24/06																																		
450			Regulator Review	30 days	Tue 7/25/06	Wed 8/23/06																																		
451			Army Respond to Comments	20 days	Thu 8/24/06	Tue 9/12/06																																		
452			Army Prepare Draft Final Report	45 days	Thu 8/24/06	Sat 10/7/06																																		
453	Primary		Submit Draft Final Report to EPA/DEQ	1 day?	Sun 10/8/06	Sun 10/8/06																																		
454																																								
455		5.2	Complete Eastern Plume Boundary Monitoring Network Design	77 days?	Mon 7/24/06	Sun 10/8/06																																		
456	Primary		Submit Draft Design	1 day?	Mon 7/24/06	Mon 7/24/06																																		
457			Regulator Review	30 days	Tue 7/25/06	Wed 8/23/06																																		
458			Army Respond to Comments	20 days	Thu 8/24/06	Tue 9/12/06																																		
459			Army Prepare Draft Final WP	45 days	Thu 8/24/06	Sat 10/7/06																																		
460	Primary		Submit Draft Final Design to EPA/DEQ	1 day?	Sun 10/8/06	Sun 10/8/06																																		
461																																								
462		5.3	Complete Eastern Plume Boundary MW Installation	182 days?	Thu 8/31/06	Wed 2/28/07																																		
463	2ndary		Submit Well Installation WP	1 day?	Thu 8/31/06	Thu 8/31/06																																		
464			Regulator Review	30 days	Fri 9/1/06	Sat 9/30/06																																		
465			Army Respond to Comments	30 days	Sun 10/1/06	Mon 10/30/06																																		
466			Army Prepare Draft Final Report	30 days	Sun 10/1/06	Mon 10/30/06																																		
467	2ndary		Submit Draft Final WP to EPA/DEQ	1 day?	Tue 10/31/06	Tue 10/31/06																																		
468																																								
469			Well Drilling	120 days	Wed 11/1/06	Wed 2/28/07																																		
470																																								
471																																								
472		6.0	Additional Investigation Work	1709 days?	Mon 12/26/05	Mon 8/30/10																																		
473		6.1	Complete Phase 1 MW-85/Johnson Creek	62 days?	Mon 12/26/05	Sat 2/25/06																																		
474	2ndary		Submit Draft Report	1 day?	Mon 12/26/05	Mon 12/26/05																																		
475			Regulator Review	30 days	Tue 12/27/05	Wed 1/25/06																																		
476			Army Respond to Comments	30 days	Thu 1/26/06	Fri 2/24/06																																		
477			Army Prepare Draft Final Report	30 days	Thu 1/26/06	Fri 2/24/06																																		
478	2ndary		Submit Draft Final Report to EPA/DEQ	1 day?	Sat 2/25/06	Sat 2/25/06																																		
479																																								
480		6.2	Bedrock Investigation	214 days?	Fri 1/29/10	Mon 8/30/10																																		
481	Primary		Submit Draft WP	1 day?	Fri 1/29/10	Fri 1/29/10																																		
482			Regulator Review	30 days	Sat 1/30/10	Sun 2/28/10																																		
483			Army Respond to Comments	30 days	Mon 3/1/10	Tue 3/30/10																																		
484			Army Prepare Draft Final WP	30 days	Mon 3/1/10	Tue 3/30/10																																		
485	Primary		Submit Draft Final WP to EPA/DEQ	1 day?	Wed 3/31/10	Wed 3/31/10																																		

**GREEN - Secondary Document submit & review period**  
**RED - Primary Document submit & review period**

## Task



## Progress



## Summary



## External Tasks



Deadline



Split

## Milestone




## Project Summary



### External Milestone



Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

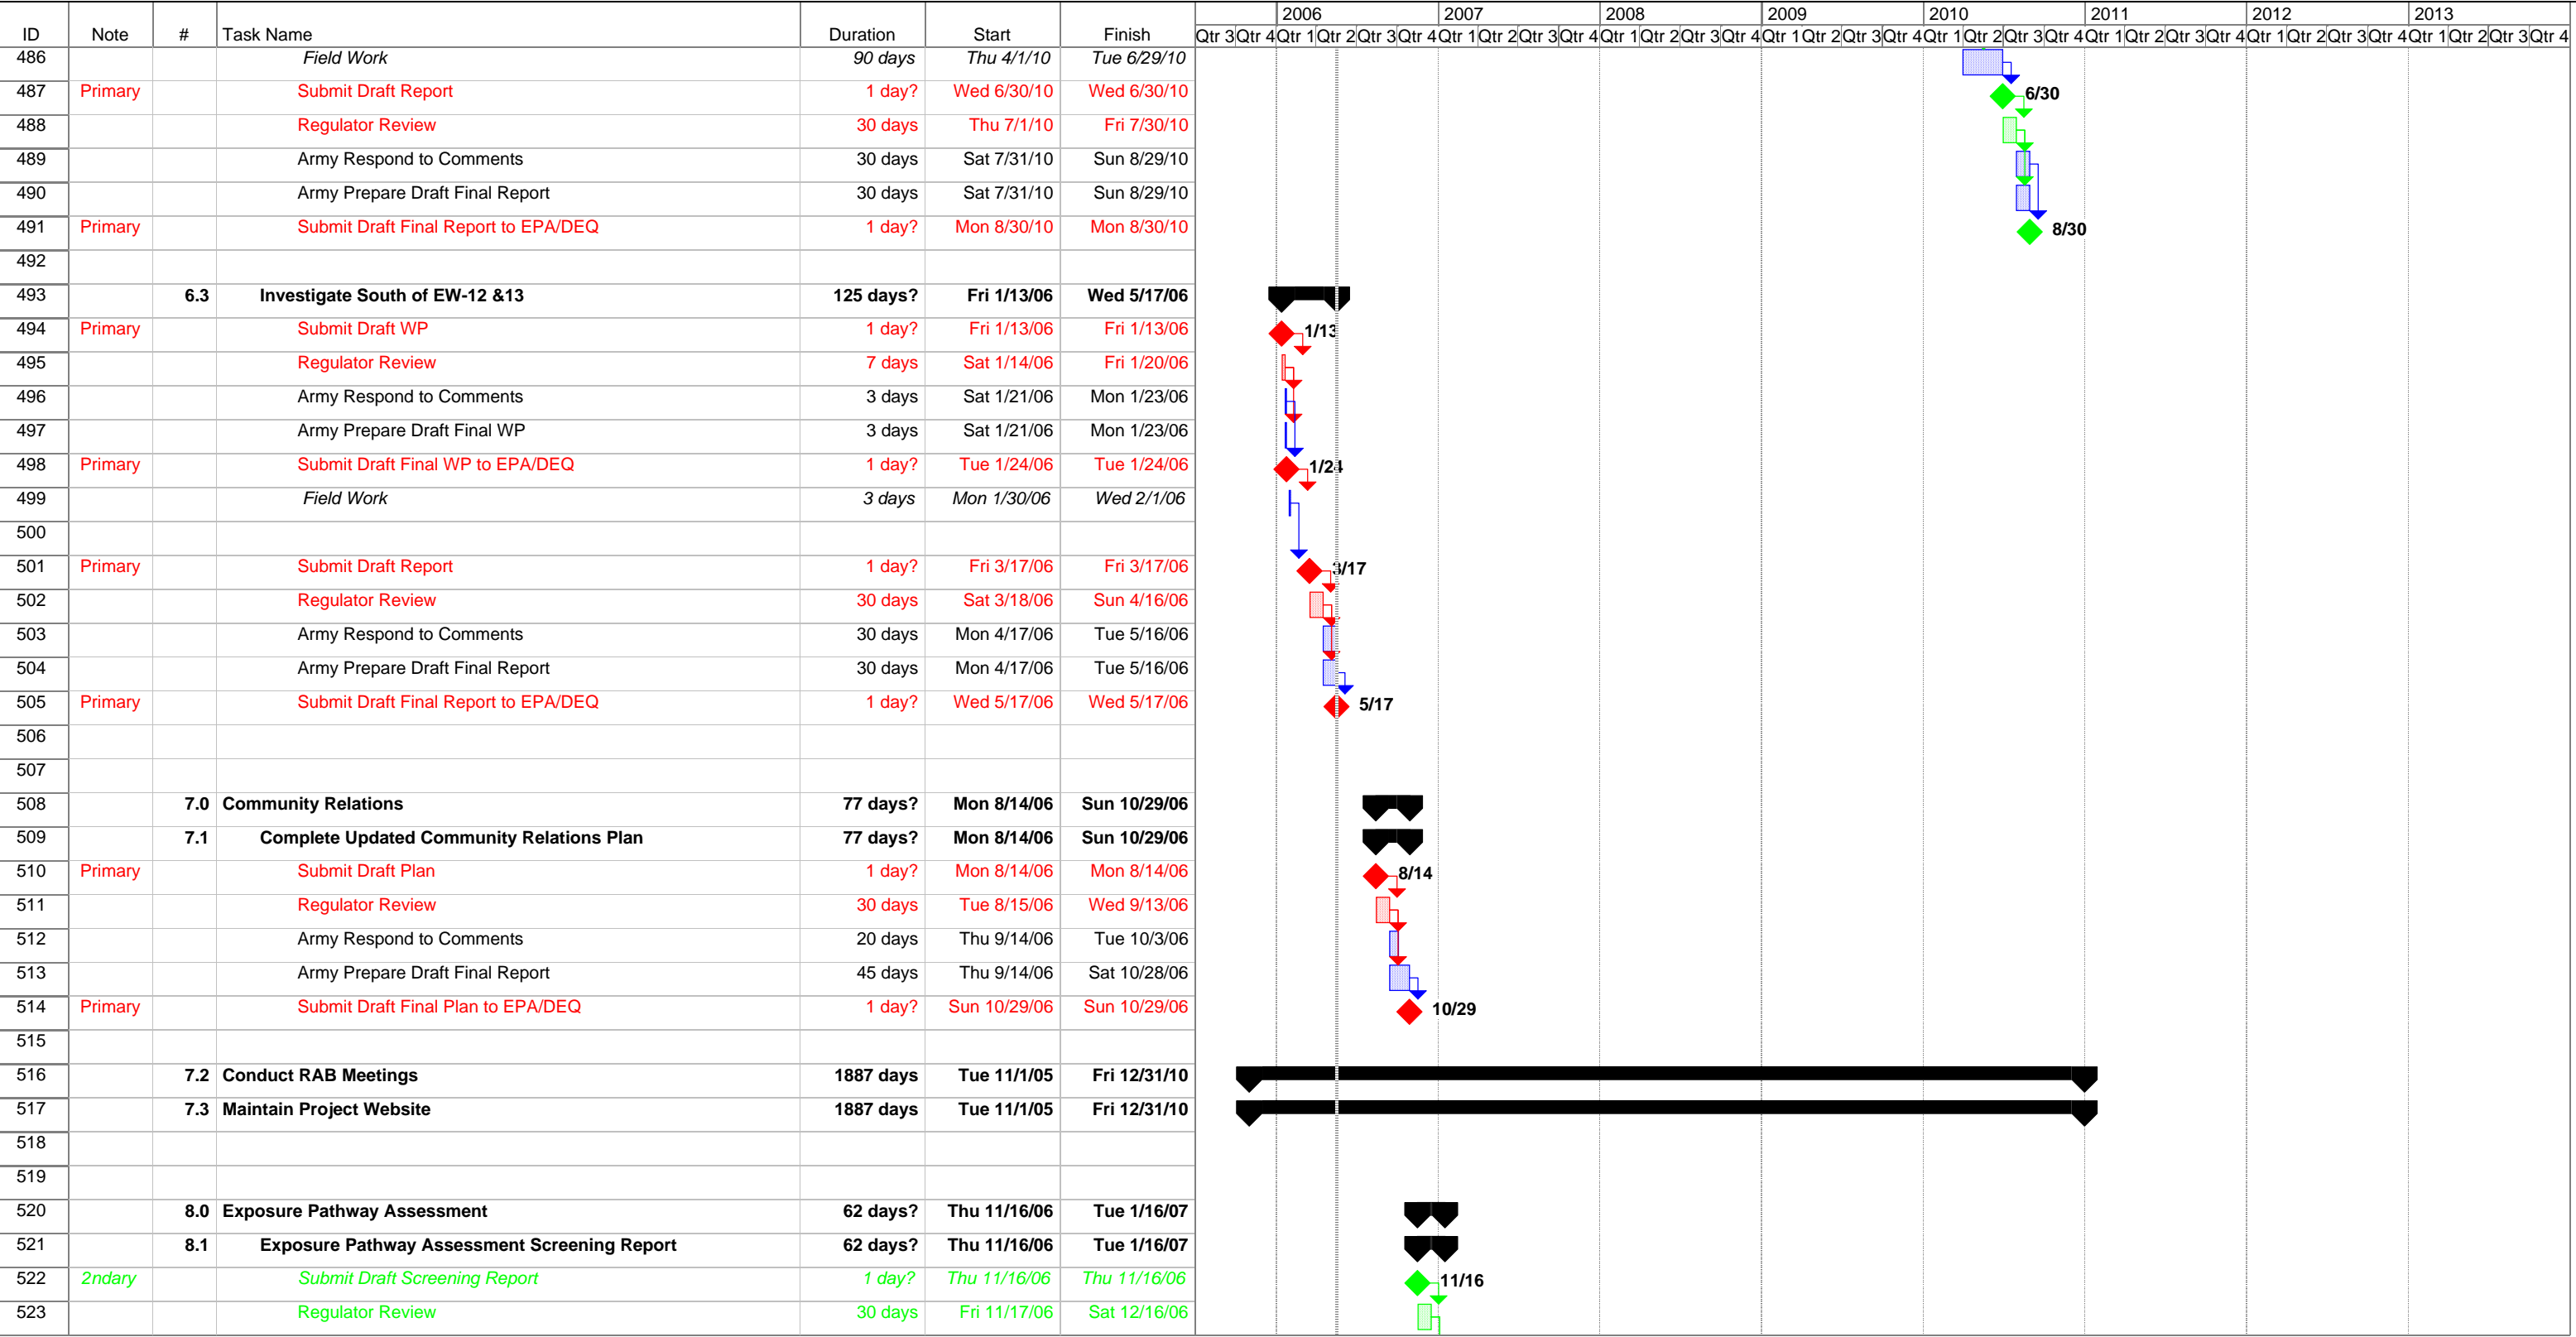

GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks


External Milestone

Deadline



Former NOP Superfund Site - Mead, NE  
Site Management Plan - SCHEDULE  
MAY 2006

ID	Note	#	Task Name	Duration	Start	Finish	2006				2007				2008				2009				2010				2011				2012				2013			
							Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		
524			Army Respond to Comments	30 days	Sun 12/17/06	Mon 1/15/07																																
525			Army Prepare Draft Final Report	30 days	Sun 12/17/06	Mon 1/15/07																																
526	2ndary		Submit Draft Final Screening Report to EPA/DEQ	1 day?	Tue 1/16/07	Tue 1/16/07																																
527																																						
528		9.0	Project Management	77 days?	Fri 7/20/07	Thu 10/4/07																																
529		9.1	5 Year Review	77 days?	Fri 7/20/07	Thu 10/4/07																																
530	Primary		Submit Draft Report	1 day?	Fri 7/20/07	Fri 7/20/07																																
531			Regulator Review	30 days	Sat 7/21/07	Sun 8/19/07																																
532			Army Respond to Comments	20 days	Mon 8/20/07	Sat 9/8/07																																
533			Army Prepare Draft Final Report	45 days	Mon 8/20/07	Wed 10/3/07																																
534	Primary		Submit Draft Final Report to EPA/DEQ	1 day?	Thu 10/4/07	Thu 10/4/07																																
535																																						
536		9.2	Routine Project Management Activities	1887 days	Tue 11/1/05	Fri 12/31/10																																



GREEN - Secondary Document submit & review period  
RED - Primary Document submit & review period

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline
