



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Egypt L&D District
Ray County, Missouri

Updated as of Feb. 21, 2013

Missouri River Area Office

Kansas City District

Schedule

Request for Assistance:	Nov. 9, 2011
Damage Survey Report:	Mar. 14, 2012
Award Date:	Nov. 28, 2012
Notice to Proceed Date:	Dec. 13, 2012
Contract Duration:	90
Contract Original Completion Date:	Mar. 12, 2013
Contract Current Completion Date:	Mar. 17, 2013
Estimated Completion Date:	Mar. 17, 2013

Progress

% Complete Actual:	23%
% Complete Schedule:	23%
Construction Contract Placement:	

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$304,403.00
Current Contract Amount:	\$304,403.00
Pending MOD Amount:	


Scope of work

Embankment and foundation seepage repair.



Project: Egypt Levee & Drainage District

River Miles: 334 to 337.9

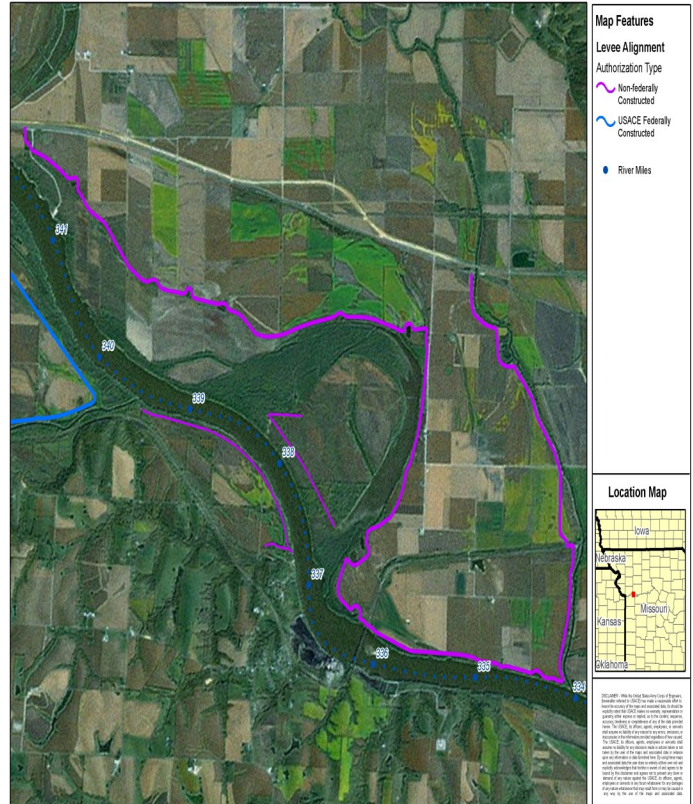

Current Progress

Awarded 11/28/12 to C L Richardson Construction Company, in the amount of \$304,403.00.

MO Valley Setback B-4 has been accepted by the Levee Board. At Tri-County, the welding is complete on the steel pipe and is ready for installation. Earthwork for this drainage structure will begin next week.

Photos
