



US Army Corps of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Tri-County District
Ray / Clay / Jackson, Missouri

Updated as of April 24, 2013

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	July 25, 2011
Damage Survey Report:	Jan. 20, 2012
Award Date:	Nov. 28, 2012
Notice to Proceed Date:	Dec. 13, 2012
Contract Duration:	90
Contract Original Completion Date:	Mar. 12, 2013
Contract Current Completion Date:	Mar. 17, 2013
Estimated Completion Date:	Mar. 17, 2013


Progress

% Complete Actual:	30%
% Complete Schedule:	30%
Construction Contract Placement:	

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$304,403.00
Current Contract Amount:	\$304,403.00
Pending MOD Amount:	

Project: Egypt Levee & Drainage District River Miles: 334 to 337.9

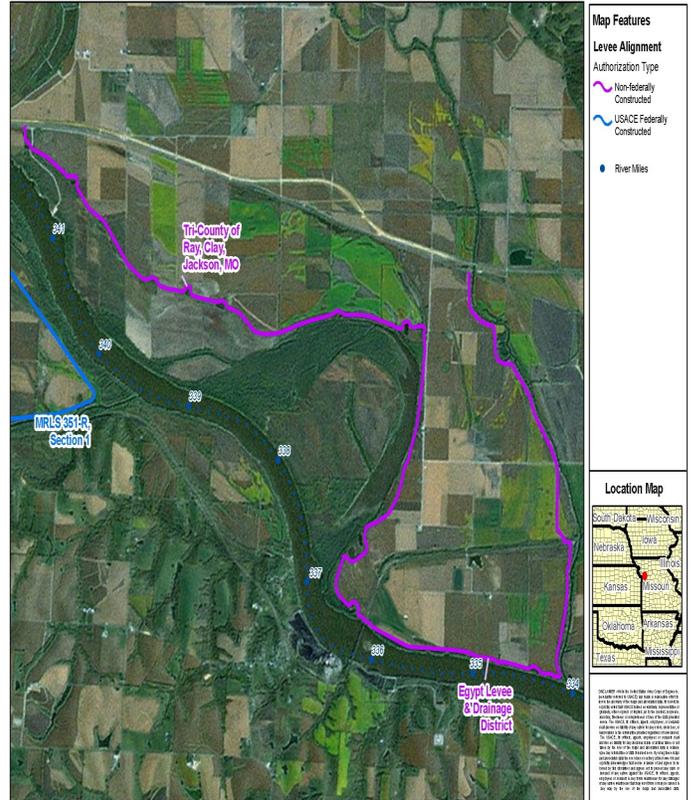

Scope of work

Drainage Structure and foundation seepage repair.

Current Progress

Awarded 11/28/12 to C L Richardson Construction Company, in the amount of \$304,403.00.

No work this week as C.L. Richardson has been having weather issues so there is no change from last week. C.L. Richardson is complete with setback levee B-4 in Missouri Valley. The contractor has completed 95% of the levee toe repairs from stations 173.20 201.25 along Jackass Bend. C.L. Richardson has acquired a new borrow area closer to the levee toe repair from station 246.50 - 254.06 which will speed up the repairs weather this week has delayed progress. Mobilization for seeding of Egypt levee district occurred this week with seeding but seeding was delayed by weather and should begin by the end of next week weather dependant.

Photos
