



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Holt County Levee District No. 9

Holt County, Missouri

Updated as of Sept. 14, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Sept. 9, 2011
Damage Survey Report:	Nov. 1, 2011
Award Date:	April 10, 2012
Notice to Proceed Date:	April 26, 2012
Contract Duration:	120
Contract Original Completion Date:	Aug. 8, 2012
Contract Current Completion Date:	Aug. 8, 2012
Estimated Completion Date:	Aug. 8, 2012


Progress

% Complete Actual:	97%
% Complete Schedule:	97%
Construction Contract Placement:	\$0.00

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$1,099,482.20
Current Contract Amount:	\$1,099,482.20
Pending MOD Amount:	\$0.00

Project: Holt County Levee District No. 9 River Miles: 486.5 to 492.4

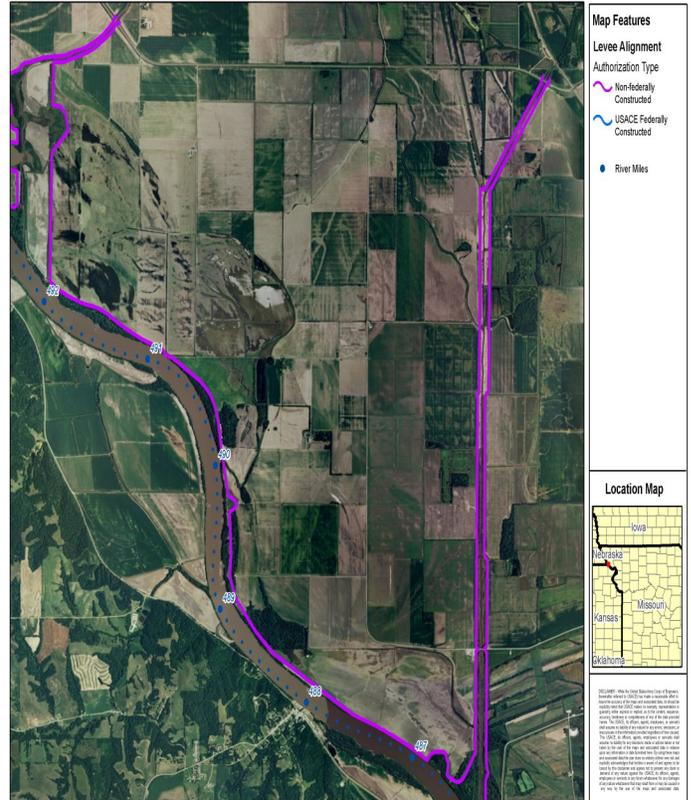

Scope of work

Breach and large scour hole repairs.

Current Progress

Contract awarded to H.B. Construction on 4/10/12. Notice to Proceed issued 4/26/12.

Final Inspection was held 9/12/12. At the conclusion, we accepted the project from the contractor with deficiencies.

Photos
