



US Army Corps  
of Engineers

# 2011 MISSOURI RIVER LEVEE REHAB UPDATE

Canon Drainage District  
Holt County, Missouri

Updated as of Sept. 26, 2012

Kansas City Residence Office

Kansas City District

## Schedule

Request for Assistance:	Aug. 25, 2011
Damage Survey Report:	Nov. 3, 2011
Award Date:	Mar. 22, 2012
Notice to Proceed Date:	Mar. 27, 2012
Contract Duration:	120
Contract Original Completion Date:	July 25, 2012
Contract Current Completion Date:	July 25, 2012
Estimated Completion Date:	July 25, 2012


## Progress

% Complete Actual:	97%
% Complete Schedule:	97%
Construction Contract Placement:	\$0.00

## Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$1,628,619.24
Current Contract Amount:	\$1,628,619.24
Pending MOD Amount:	\$0.00

Project: Canon Drainage District and Kimsey Holly Creek River Miles: 455.9 to 486.4

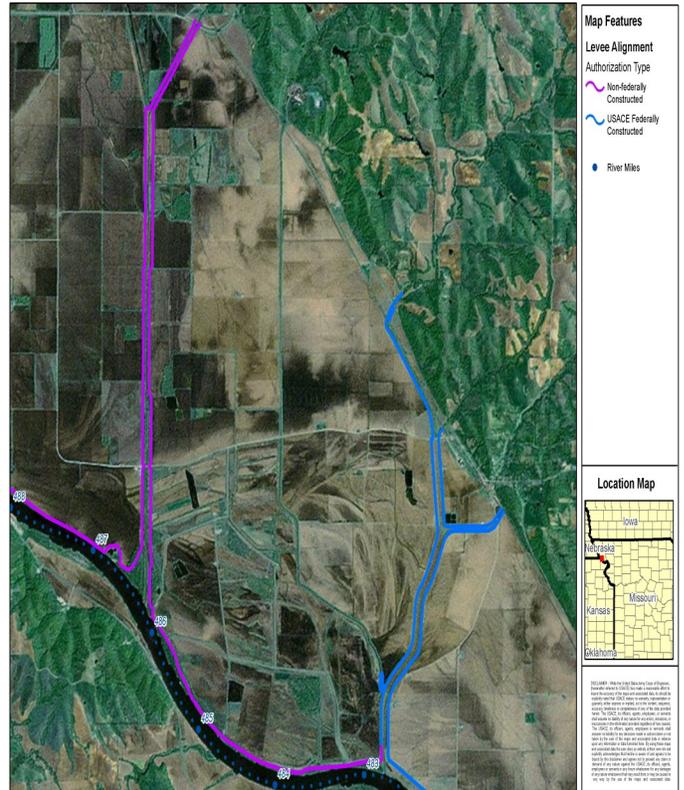

## Scope of work

Levee rehabilitation work is the repair of the crown, landside, and riverside levee and adjacent area from flood damage. This includes rebuilding two sections where the 2011 flood breached the levee and filling the associated scour by the breaches. Work includes stone placement, replacement of damage steel pipes, gravel placement, seeding and mulching.

**Current Progress**

The Pre-construction meeting was held 3/23/12. Notice to proceed was issued 3/27/12. The Mutual Understanding Meeting is also being held on 3/27/12.

Level of protection reached on 6/2/12. Final inspection on 6/12/12 resulted in accepted the work with seeding as a possible deficiency, as outside the seeding window. ESI started seeding last week and plans to complete seeding the areas of concern this week.

**Photos**

