



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Lower Chariton
Chariton County, Missouri

Updated as of Oct. 26, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Oct 1, 2011
Damage Survey Report:	Oct 26, 2011
Award Date:	Sept. 5, 2012
Notice to Proceed Date:	Aug. 21, 2012
Contract Duration:	60
Contract Original Completion Date:	Oct. 15, 2012
Contract Current Completion Date:	Oct. 15, 2012
Estimated Completion Date:	Oct. 15, 2012


Progress

% Complete Actual:	98%
% Complete Schedule:	98%
Construction Contract Placement:	

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$198,400.51
Current Contract Amount:	\$198,400.51
Pending MOD Amount:	

Project: Lower Chariton River Levee District River Miles: 242.4 to 227.4

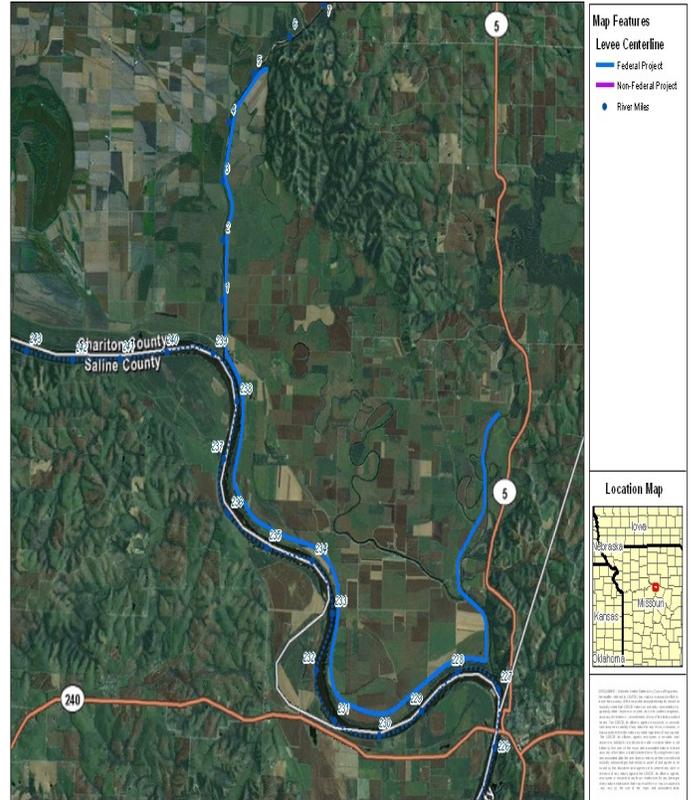

Scope of work

Repair erosion damage around five inlet structures near stations 7+75, 74+00, 137+85, 179+00, and 219+50.
Install new vertical gage near station 179+00.

Current Progress

Lower Chariton Rock Placement contract was awarded to Wolfe Construction for \$89,440 on 8/7/12.

The Levee Seeding Contract was awarded to Prudent Technologies, Inc. of Kansas City, Missouri on 9/5/12, for \$198,400.51 to complete levee/seeding repairs at MRLS 513-512-R, MRLS 500-R, MRLS 482-R, Henry Pohl and Lower Chariton Levees.

The final inspection was held on 9/26/12. Deficiencies were noted with the vertical gages. The deficiencies with the vertical gates noted during the final inspection have been corrected. All work is complete except for final evaluation of the grass-stand.

Photos
