



US Army Corps  
of Engineers

# 2011 MISSOURI RIVER LEVEE REHAB UPDATE

Henry Pohl Levee  
Atchison County, Kansas

Updated as of Nov. 2, 2012

Kansas City Residence Office

Kansas City District

## Schedule

Request for Assistance:	Nov. 14, 2011
Damage Survey Report:	Jan. 20, 2012
Award Date:	Sept. 5, 2012
Notice to Proceed Date:	TBD
Contract Duration:	120
Contract Original Completion Date:	Jan. 17, 2013
Contract Current Completion Date:	Jan. 17, 2013
Estimated Completion Date:	Jan. 17, 2013


## Progress

% Complete Actual:	90%
% Complete Schedule:	90%
Construction Contract Placement:	

## Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$198,400.51
Current Contract Amount:	\$198,400.51
Pending MOD Amount:	

Project: Henry Pohl Levee River Miles: 410.8 to 412

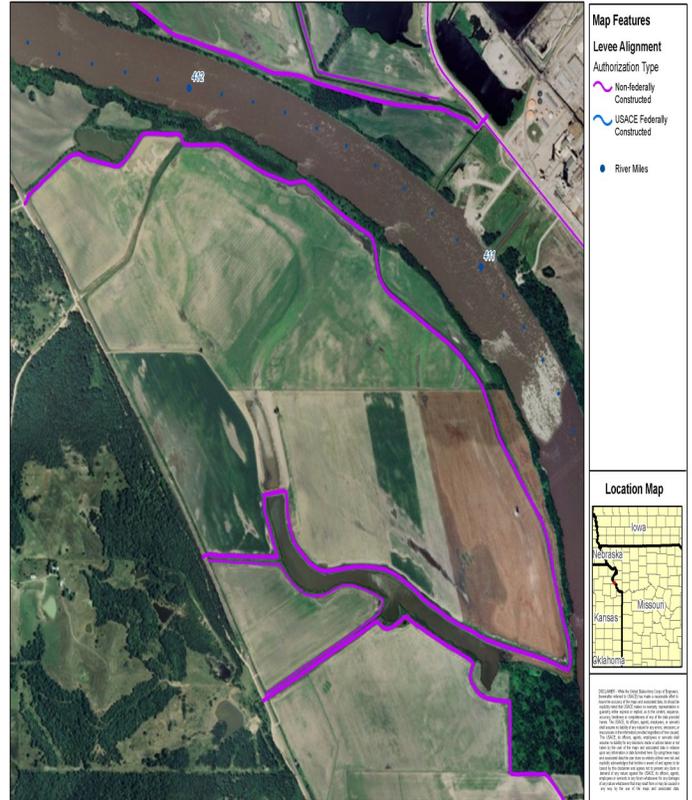

## Scope of work

Overtopping and significant embankment erosion repair.

***Current Progress***

The Levee Seeding Contract was awarded to Prudent Technologies, Inc. of Kansas City, Missouri on 9/5/12, for \$198,400.51 to complete levee/seeding repairs at MRLS 513-512-R, MRLS 500-R, MRLS 482-R, Henry Pohl and Lower Chariton Levees.

Prudent Technologies has completed all work to included the seeding and earthwork at Henry Pohl. Quality Assurance personnel final inspection of the work at Henry Pohl.

***Photos***
