



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

MRLS 482 - R
Doniphan, Kansas

Updated as of Nov. 15, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Oct. 11, 2011
Damage Survey Report:	Jan. 24, 2012
Award Date:	Sept. 5, 2012
Notice to Proceed Date:	TBD
Contract Duration:	120
Contract Original Completion Date:	Jan. 17, 2013
Contract Current Completion Date:	Jan. 17, 2013
Estimated Completion Date:	Jan. 17, 2013


Progress

% Complete Actual:	95%
% Complete Schedule:	95%
Construction Contract Placement:	

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$198,400.51
Current Contract Amount:	\$198,400.51
Pending MOD Amount:	

Project: MRLS 482-R River Miles: 458.0 to 467.0

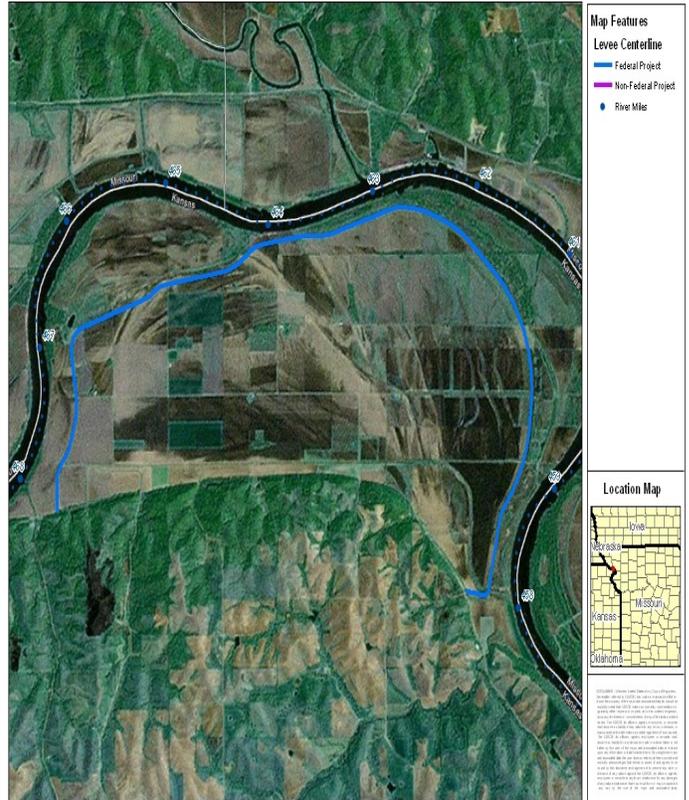

File: C:\Data\Project 482\Info\GIS\Info2\Legend\1\F_MRLS482R\Levee_Rehab_Map_Sum

Scope of work

Seeding and Mulching

Current Progress

The Levee Seeding Contract was awarded to Prudent Technologies, Inc. of Kansas City, Missouri on 9/5/12, for \$198,400.51 to complete levee/seeding repairs at MRLS 513-512-R, MRLS 500-R, MRLS 482-R, Henry Pohl and Lower Chariton Levees.

We inspected the grass-stand. Acceptable growth with a minimal isolated bare areas was shown.

Photos
