



US Army Corps of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

KS Department of Corrections
Leavenworth, KS

Updated as of Nov. 29, 2012

Kansas City Residence Office

Kansas City District

Schedule

| | |
|------------------------------------|---------------|
| Request for Assistance: | Jul. 25, 2011 |
| Damage Survey Report: | Jan. 19, 2012 |
| Award Date: | Apr. 5, 2012 |
| Notice to Proceed Date: | Apr. 23, 2012 |
| Contract Duration: | 120 |
| Contract Original Completion Date: | Aug. 11, 2012 |
| Contract Current Completion Date: | Aug. 11, 2012 |
| Estimated Completion Date: | Aug. 11, 2012 |


Progress

| | |
|----------------------------------|-----|
| % Complete Actual: | 95% |
| % Complete Schedule: | 95% |
| Construction Contract Placement: | |

Funding

| | |
|--------------------------|-----------------------|
| Funds Source: | FCCE – Rehabilitation |
| Award Contract Amount: | |
| Current Contract Amount: | |
| Pending MOD Amount: | |

Project: Kansas Department of Corrections River Miles: 387.3 to 396.6

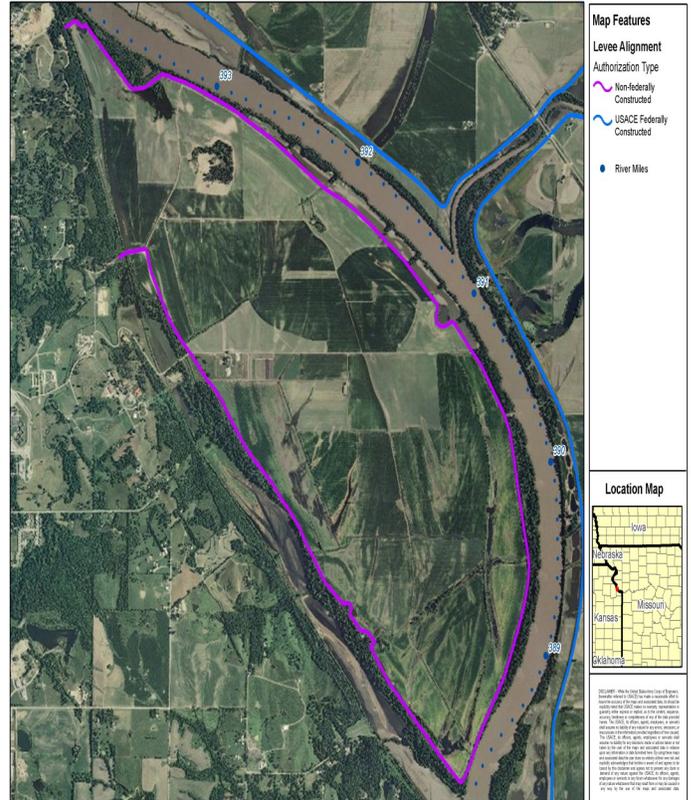

Scope of work

Breach and large scour hole repairs.

Current Progress

Project Information Report was approved by Northwest Division on 2/8/12. Notice to Proceed was issued 4/23/12.

Final inspection was held on 11/20/12. There are a few deficiencies related to seeding that will need to be addressed during the spring seeding season.

Photos
