



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Grape-Bolin-Schwartz Levee
Leavenworth, Kansas

Updated as of Aug. 20, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Sept. 29, 2011
Damage Survey Report:	Jan. 19, 2012
Award Date:	May 9, 2012
Notice to Proceed Date:	TBD
Contract Duration:	60
Contract Original Completion Date:	Aug. 3, 2012
Contract Current Completion Date:	Aug. 3, 2012
Estimated Completion Date:	Aug. 3, 2012


Progress

% Complete Actual:	100%
% Complete Schedule:	100%
Construction Contract Placement:	\$0.00

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$141,500.89
Current Contract Amount:	\$141,500.89
Pending MOD Amount:	\$0.00

Project: Grape-Bollin-Schwartz Levee Association River Miles: 405.8 to 409.7

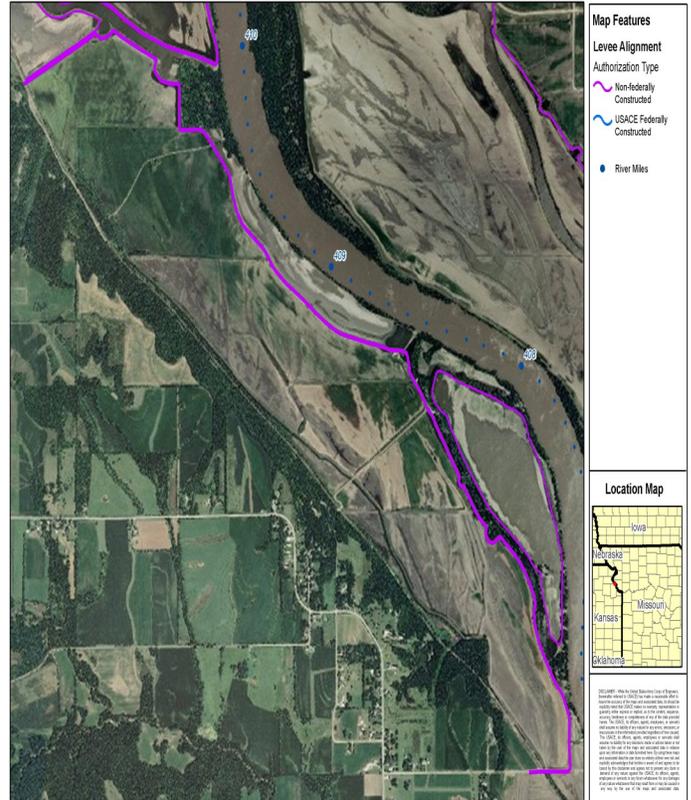

Scope of work

Breach and large scour hole repair.

Current Progress

Contracting Status: Awarded to Coastal Engineering for \$141,500.89 on 5/9/12.

Coastal Environmental Group received their approve Notice of Intent from KDHE on 6/7/12.

The southernmost breach is complete. The 36" Flap gate is installed. The southern setback and erosion repair just north of the southern setback are complete. The erosion repair (in-place breach repair) on the northern end has the impervious cap 100% in place. Gravel has been placed on northern access ramps. Representatives from Costal, the Kansas City Resident Office, and the Levee Board conducted a final inspection on 7/31/12. Project 100% complete and working on the contract closeout process.

Photos
