



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Henrietta-Crooked River, Sec 1
Ray County, Missouri

Updated as of Aug. 23, 2012

Missouri River Area Office

Kansas City District

Schedule

Request for Assistance:	Sept. 1, 2011
Damage Survey Report:	Feb. 9, 2012
Award Date:	May 22, 2012
Notice to Proceed Date:	June 6, 2012
Contract Duration:	70
Contract Original Completion Date:	Aug. 9, 2012
Contract Current Completion Date:	Aug. 9, 2012
Estimated Completion Date:	Aug. 9, 2012


Progress

% Complete Actual:	95%
% Complete Schedule:	95%
Construction Contract Placement:	\$0.00

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$53,086.00
Current Contract Amount:	\$53,086.00
Pending MOD Amount:	\$0.00

Project: Baltimore Cherry Miles Ray Henrietta Crooked River Miles: 300.3 to 302.2

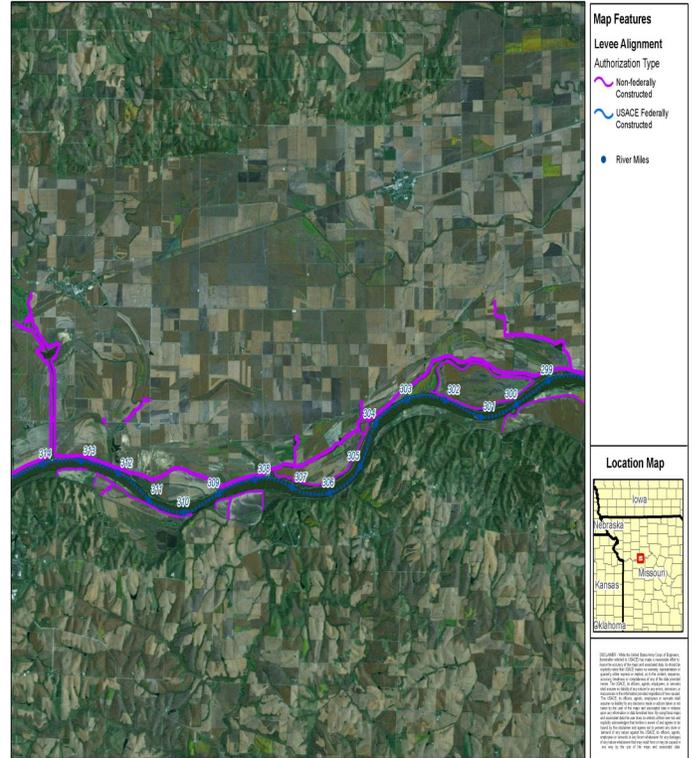

Scope of work

Embankment and foundation seepage repair.

Current Progress

Contract awarded 5/22/12 to Tri-Smith Construction, LLC for \$53,086.

Contractor is 100% complete with all earthwork, only seeding remains.

Photos

