



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Rushville/Sugarlake Levee
Buchanan/ Platte County, Missouri

Updated as of May 16, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Sept. 11, 2011
Damage Survey Report:	Oct. 22, 2011
Award Date:	Jan. 1, 2012
Notice to Proceed Date:	Feb. 1, 2012
Contract Duration:	120
Contract Original Completion Date:	May 31, 2012
Contract Current Completion Date:	May 31, 2012
Actual Completion Date:	Apr. 20, 2012


Progress

% Complete Actual:	100%
% Complete Schedule:	100%
Construction Contract Placement:	\$658,081.22

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$1,283,668.00
Current Contract Amount:	\$1,283,668.00
Pending MOD Amount:	\$0.00

Project: Platte Cty DD 1 sec 1 Rushville Sugar lake River Miles: 418.2 to 422.6

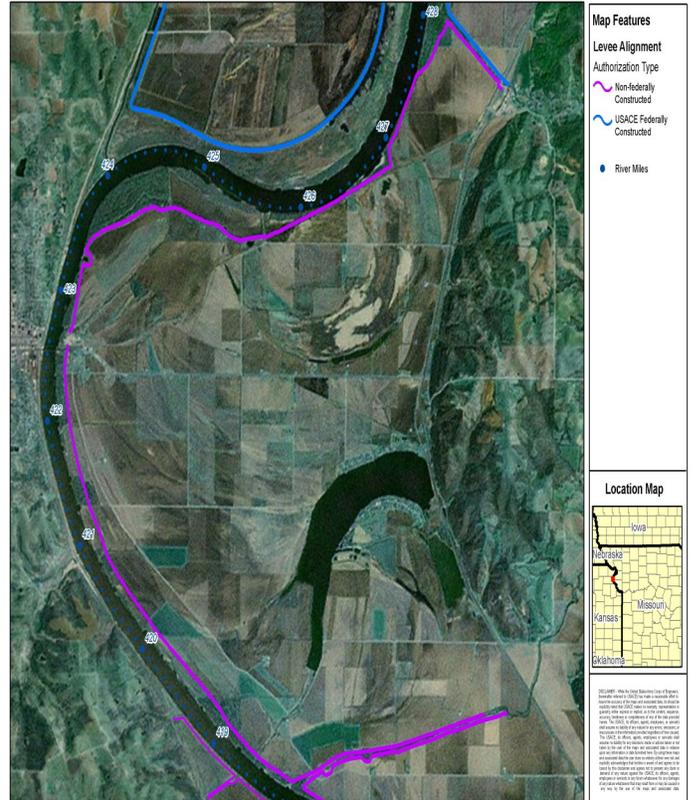

Scope of work

Levee breach and large scour hole repairs.

Current Progress

Awarded to ESI on 1/30/12. Notice to proceed was issued on 2/1/12.

Level of Protection was restored on 3/18. Final Inspection was held 4/20/12, and all deficiencies corrected. Project is complete.

Photos
