



US Army Corps  
of Engineers

# 2011 MISSOURI RIVER LEVEE REHAB UPDATE

Saline County No. 2  
Saline County, Missouri

Updated as of June 13, 2012

Kansas City Residence Office

Kansas City District

## Schedule

Request for Assistance:	Nov. 17, 2011
Damage Survey Report:	Jan. 24, 2012
Award Date:	May 10, 2012
Notice to Proceed Date:	May 10, 2012
Contract Duration:	70
Contract Original Completion Date:	July 29, 2012
Contract Current Completion Date:	July 29, 2012
Estimated Completion Date:	July 29, 2012


## Progress

% Complete Actual:	95%
% Complete Schedule:	95%
Construction Contract Placement:	0

## Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$28,975.00
Current Contract Amount:	\$28,975.00
Pending MOD Amount:	

Project: Saline County Levee District No. 2 River Miles: 242.5 to 251.6

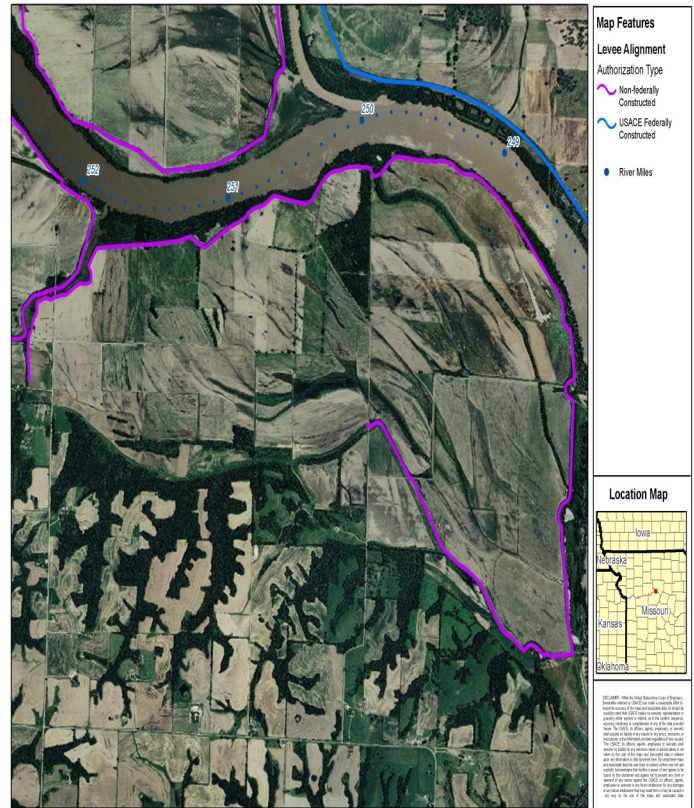

## Scope of work

Repair the damaged area (compromised landside levee toe slope) by “fortifying” (flattening) the existing mid to lower landside slope to a 1-foot vertical on 8-feet horizontal slope to toe out. The flattened slope will commence (spring point) at varying heights ranging from 4 to 5-feet down from levee crown crest, depending upon height of the embankment. The riverside levee slope will be seeded and mulched.

***Current Progress***

Saline County No. 2 Levee Rehab Contract was awarded to R&L Boone Construction for \$28,975.

Construction is complete as of 6/11/12. Work accepted with seeding as a possible deficiency since we are outside the seeding window.

***Photos***
