



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Sugar Tree Bottom
Carroll County, Missouri

Updated as of Aug. 20, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Sept. 28, 2011
Damage Survey Report:	Oct. 17, 2011
Award Date:	May 22, 2012
Notice to Proceed Date:	May 31, 2012
Contract Duration:	120
Contract Original Completion Date:	Sept. 28, 2012
Contract Current Completion Date:	Sept. 28, 2012
Estimated Completion Date:	Sept. 28, 2012


Progress

% Complete Actual:	95%
% Complete Schedule:	95%
Construction Contract Placement:	\$0.00

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$73,496
Current Contract Amount:	\$73,496
Pending MOD Amount:	\$0.00

Project: Sugartree Bottom Levee District River Miles: 288.2 to 298.4

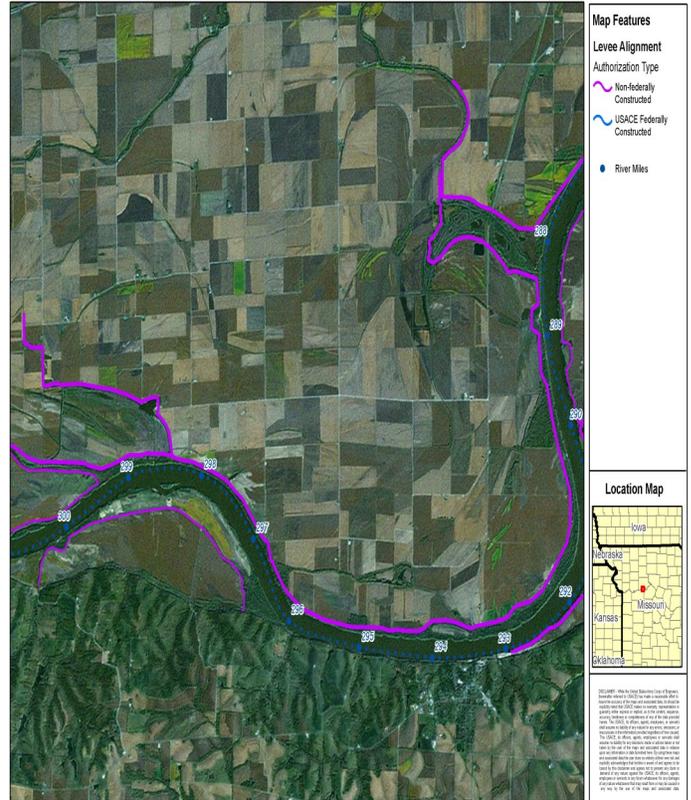

Scope of work

The recommended repair action consist of in-place repair of intermittent riverside slope erosion; repair of compromised (weakened) landside lower toe slope/line; repair of landside slope embankment failure (slide); and seeding/mulching of riverside embankment.

Current Progress

Contract award to Tri-Smith Construction, LLC for \$73,496 on 5/22/12.

All work is complete except for seeding.

Photos

