

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Wakenda Levee Repair Carroll County, Missouri

Updated as of May 9, 2012

Kansas City District

Missouri River Area Office

Schedule

Request for Assistance:

Damage Survey Report:

Award Date:

Notice to Proceed Date:

Contract Duration:

Contract Original Completion Date:

Contract Current Completion Date:

Estimated Completion Date:

Mug. 26, 2011

Sept. 30, 2011

Jan. 23, 2012

Jan. 25, 2012

May 1, 2012

May 20, 2012


May 20, 2012

Progress

% Complete Actual: 70%
% Complete Schedule: 70%
Construction Contract Placement: \$124,315.00

Funding

Funds Source: FCCE – Rehabilitation
Award Contract Amount: \$722,763.00
Current Contract Amount: \$722,763.00
Pending MOD Amount: \$0.00

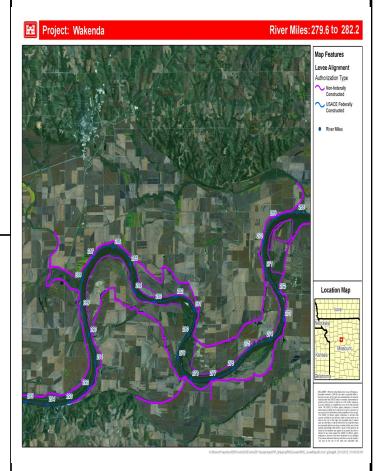

Scope of work

Levee breach and large scour hole repairs.

| Kansas City Resident Office | Kansas City Distri |
|--|----------------------------|
| Current Progress | |
| Contract Awarded to Ideker, Inc. on 1/23/12. Notice to proceed was issued on 1/25/201 | 2. |
| evel of protection was achieved by 3/15/12. | |
| Vork on sand boils and toe repairs took place last week until 4/13/12 when rain preven | ted work. |
| Seeding is completed short some minor fertilization. Final inspection is being schedul slignment and cross section is under way. | led. Confirmation survey o |
| | |
| | |
| | |
| | |
| | |
| | |
| Photos Communication of the Co | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
