



US Army Corps  
of Engineers

# 2011 MISSOURI RIVER LEVEE REHAB UPDATE

Cooper County Levee District 1  
Cooper County, Missouri

Updated as of Feb. 21, 2013

Kansas City Residence Office

Kansas City District

## Schedule

Request for Assistance:	Nov. 9, 2011
Damage Survey Report:	June 1, 2012
Award Date:	Jan. 25, 2013
Notice to Proceed Date:	Feb. 6, 2013
Contract Duration:	45 days
Contract Original Completion Date:	Mar. 23, 2013
Contract Current Completion Date:	Mar. 23, 2013
Estimated Completion Date:	Mar. 23, 2013


## Progress

% Complete Actual:	1%
% Complete Schedule:	1%
Construction Contract Placement:	

## Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$31,077.50
Current Contract Amount:	\$31,077.50
Pending MOD Amount:	

Project: Levee District No. 1 of Cooper County River Miles: 177 to 186.1

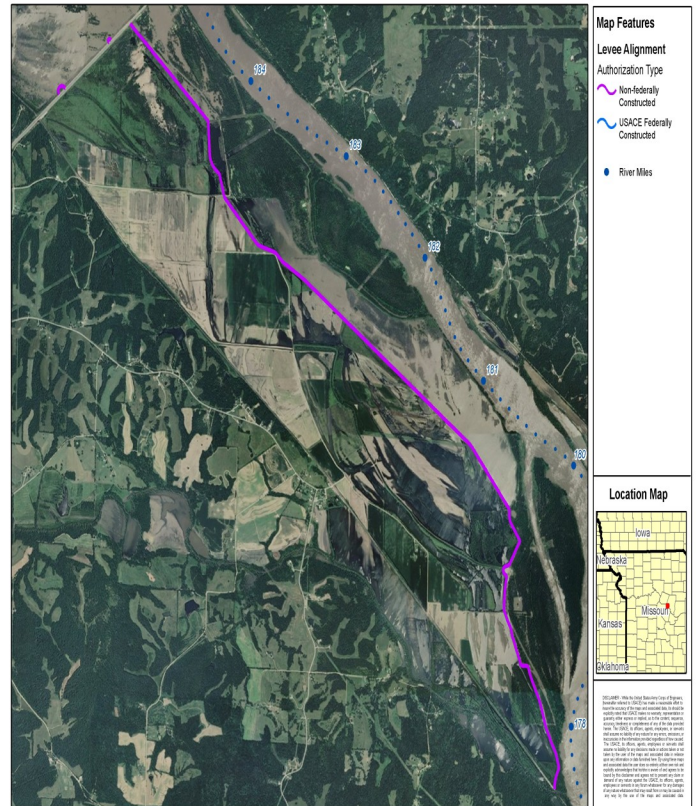

## Scope of work

Repair of slope embankment failure and reseeding.

***Current Progress***

Contract was awarded to C.L. Richardson for \$31,077.50 on January 25, 2013.

CL Richardson has begun brush hogging the levee and clearing and grubbing for slope repairs near STA 385+00. Wet conditions are slowing progress.

***Photos***
