



US Army Corps  
of Engineers

# 2011 MISSOURI RIVER LEVEE REHAB UPDATE

Belcher-Lozier Levee District  
Carroll County, Missouri

Updated as of Sept. 20, 2012

Missouri River Area Office

Kansas City District

## Schedule

Request for Assistance:	Aug. 26, 2011
Damage Survey Report:	Oct. 28, 2011
Award Date:	June 21, 2012
Notice to Proceed Date:	June 28, 2012
Contract Duration:	90
Contract Original Completion Date:	Sept 26, 2012
Contract Current Completion Date:	Sept 26, 2012
Estimated Completion Date:	Sept 26, 2012


## Progress

% Complete Actual:	100%
% Complete Schedule:	100%
Construction Contract Placement:	

## Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$291,849.40
Current Contract Amount:	\$291,849.40
Pending MOD Amount:	

Project: Baltimore Cherry Miles Ray Henrietta Crooked River Miles: 300.3 to 302.2

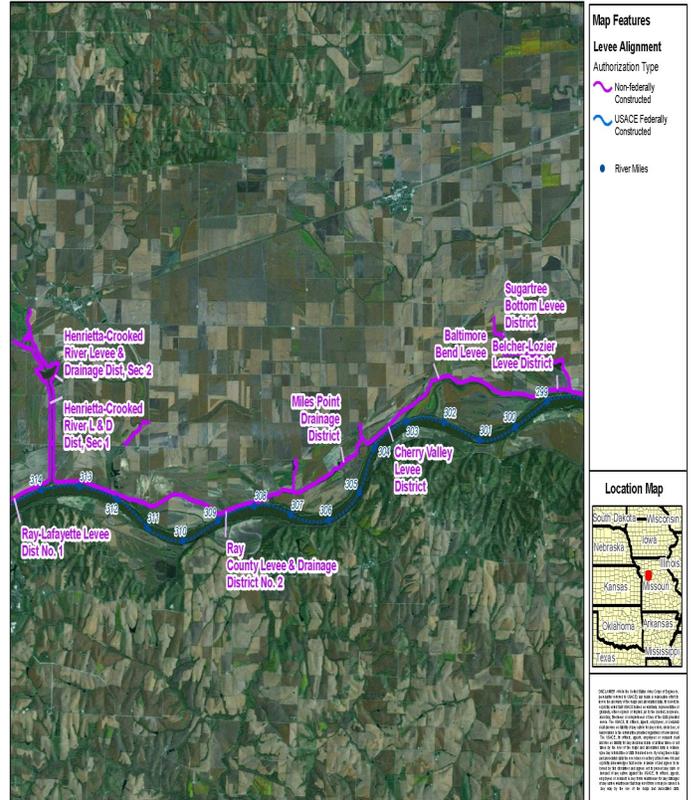

## Scope of work

Belcher-Lozier Levee Unit is part of the levee system with Baltimore Bend, Miles Point, Ray County, Henrietta-Crooked River, Section 2 and Cherry Valley Levee Units. Repairs consist of erosion repair and reseeding / mulching.

***Current Progress***

Belcher-Lozier was awarded to Widel construction for \$291,849.40 on 6/21/12. Pre-Construction meeting held on 6/26/12. Notice to Proceed was issued on 6/28/12.

The final inspection was held on 9/6/12. There was only one deficiency noted and the contractor corrected it immediately following the inspection. The project was accepted as completed. The project has been accepted.

***Photos***
