



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Kimsey Holly Levee District
Holt County, Missouri

Updated as of Oct. 4, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	July 20, 2011
Damage Survey Report:	Nov. 3, 2011
Award Date:	March 22, 2012
Notice to Proceed Date:	March 27, 2012
Contract Duration:	120
Contract Original Completion Date:	July 25, 2012
Contract Current Completion Date:	July 25, 2012
Estimated Completion Date:	July 25, 2012


Progress

% Complete Actual:	100%
% Complete Schedule:	100%
Construction Contract Placement:	\$0.00

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	Not Awarded
Current Contract Amount:	Not Awarded
Pending MOD Amount:	\$0.00

Project: Canon Drainage District and Kimsey Holly Creek River Miles: 455.9 to 486.4

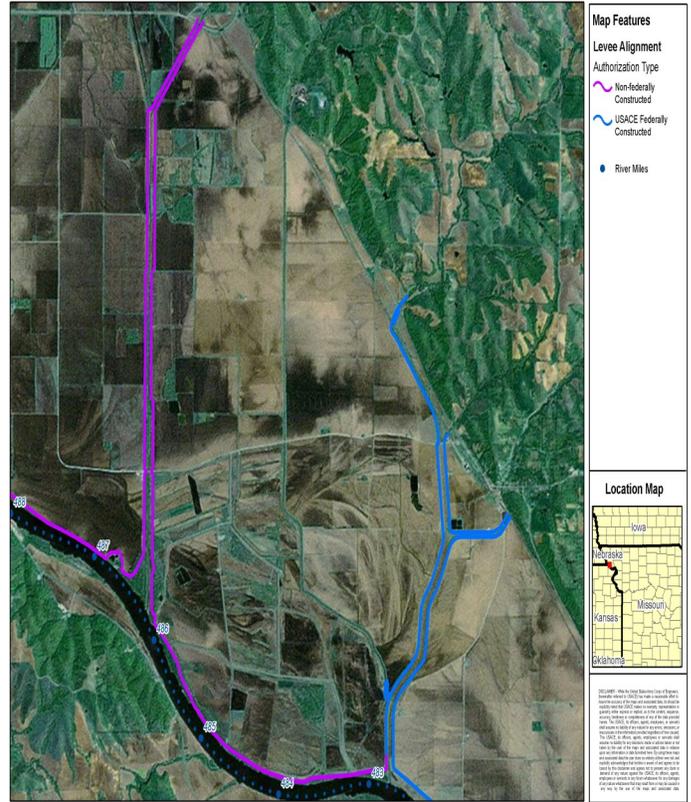

Scope of work

Repair consists of reseeding and mulching the grass kill areas and repairing the scour with impervious fill.

Current Progress

Level of protection reached on 6/2/12. Final inspection was held on 6/12/12. ESI reseeded and is complete. The project is 100% complete.

Photos
