



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Cambridge
Saline County, Missouri

Updated as of Dec. 20, 2012

Kansas City Residence Office

Kansas City District

Schedule

Request for Assistance:	Oct. 4, 2011
Damage Survey Report:	Mar. 14, 2012
Award Date:	Dec. 19, 2012
Notice to Proceed Date:	TBD
Contract Duration:	TBD
Contract Original Completion Date:	TBD
Contract Current Completion Date:	TBD
Estimated Completion Date:	TBD


Progress

% Complete Actual:	
% Complete Schedule:	
Construction Contract Placement:	

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	\$98,999
Current Contract Amount:	\$98,999
Pending MOD Amount:	

Project: Cambridge Levee Assn., Inc. (NFP) River Miles: 231.3 to 235

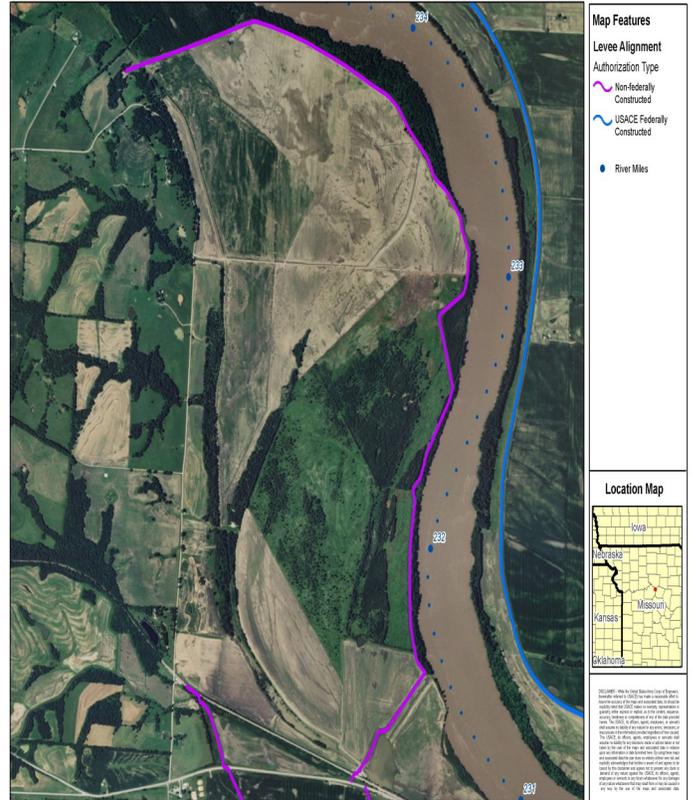

Scope of work

Repair (re-grading) of riverside slope and repair of destroyed (lost) sod cover damage by seeding and mulching.
Replace damaged 54-inch corrugated metal pipe at drainage structure station 205+00.

Current Progress

Levee Rehab Contract for Cambridge Levee Association was awarded 12/19/12 to Wayne Brown Enterprises, of Gilliam, Missouri, in the amount of \$98,999.

Photos
