



US Army Corps  
of Engineers

# 2011 MISSOURI RIVER LEVEE REHAB UPDATE

Cherry Valley Levee  
Carroll County, Missouri

Updated as of Aug. 23, 2012

Missouri River Area Office

Kansas City District

## Schedule

Request for Assistance:	Aug. 26, 2011
Damage Survey Report:	Oct. 28, 2011
Award Date:	June 21, 2012
Notice to Proceed Date:	June 28, 2012
Contract Duration:	90
Contract Original Completion Date:	Sept 26, 2012
Contract Current Completion Date:	Sept 26, 2012
Estimated Completion Date:	Sept 26, 2012


## Progress

% Complete Actual:	70%
% Complete Schedule:	70%
Construction Contract Placement:	

## Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	
Current Contract Amount:	
Pending MOD Amount:	

Project: Baltimore Cherry Miles Ray Henrietta Crooked River Miles: 300.3 to 302.2

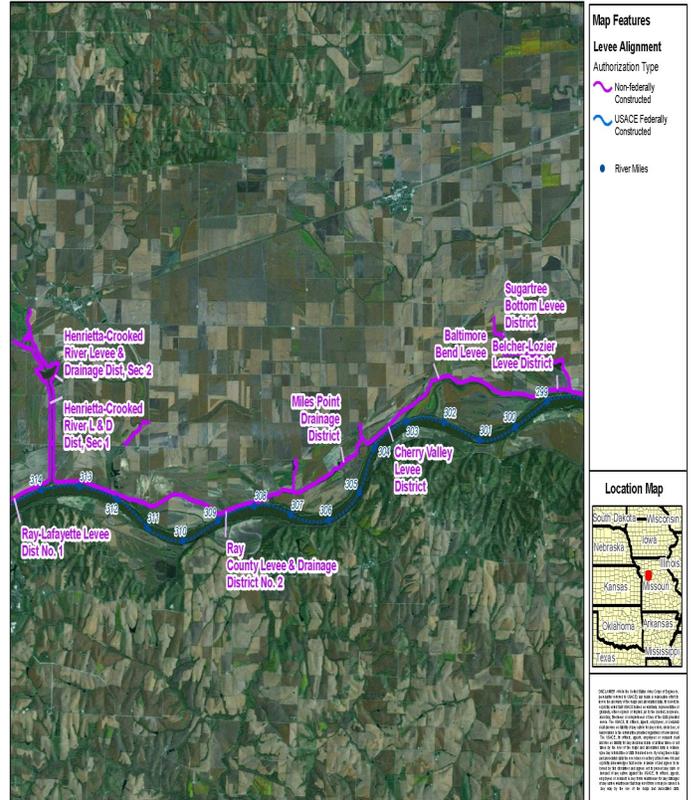

## Scope of work

Cherry Valley Levee Unit is part of the levee system with Belcher-Lozier, Miles Point, Ray County, Henrietta-Crooked River, Section 2 and Baltimore Bend County Levee Units. Repairs consist of erosion repair and reseeding / mulching.

***Current Progress***

A preparatory meeting was held for the slope repairs on the setback at the upstream end. No work has been performed yet.

***Photos***
