



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Miles Point Drainage
Carroll County, Missouri

Updated as of Aug. 23 , 2012

Missouri River Area Office

Kansas City District

Schedule

| | |
|------------------------------------|---------------|
| Request for Assistance: | Aug. 26, 2011 |
| Damage Survey Report: | Oct. 28, 2011 |
| Award Date: | June 21, 2012 |
| Notice to Proceed Date: | June 28, 2012 |
| Contract Duration: | 90 |
| Contract Original Completion Date: | Sept 26, 2012 |
| Contract Current Completion Date: | Sept 26, 2012 |
| Estimated Completion Date: | Sept 26, 2012 |


Progress

| | |
|----------------------------------|-----|
| % Complete Actual: | 70% |
| % Complete Schedule: | 70% |
| Construction Contract Placement: | |

Funding

| | |
|--------------------------|-----------------------|
| Funds Source: | FCCE – Rehabilitation |
| Award Contract Amount: | |
| Current Contract Amount: | |
| Pending MOD Amount: | |

Project: Baltimore Cherry Miles Ray Henrietta Crooked River Miles: 300.3 to 302.2

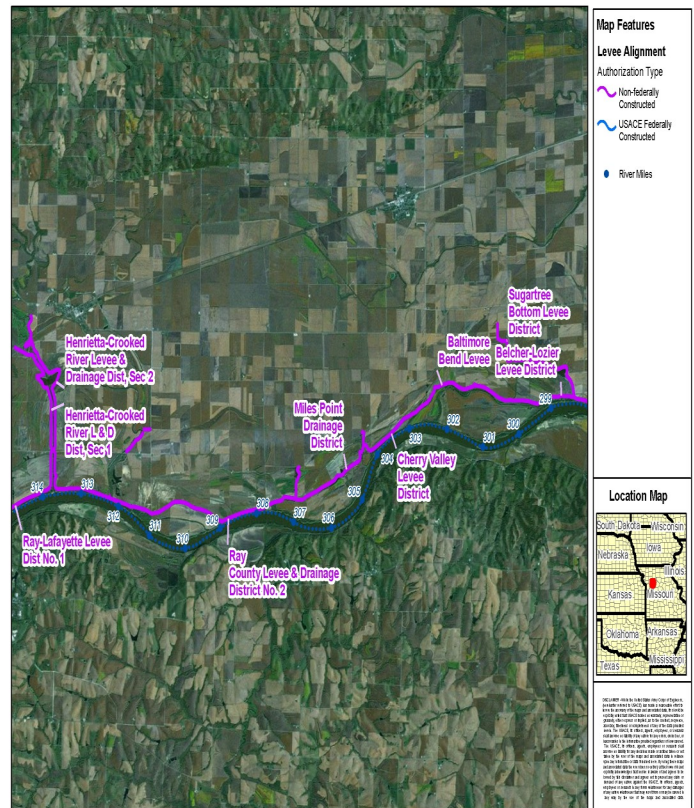

Scope of work

Miles Point Drainage Levee Unit is part of the levee system with Belcher-Lozier, Cherry Valley, Ray County, Henrietta-Crooked River, Section 2 and Baltimore Bend County Levee Units. Repairs consist of seepage and erosion repair.

Current Progress

Widel has finished construction of underseepage berm and has completed slope repairs. Seeding/mulching remains.

Photos
