



US Army Corps
of Engineers

2011 MISSOURI RIVER LEVEE REHAB UPDATE

Ray County Levee
Ray County, Missouri

Updated as of Aug. 23, 2012

Missouri River Area Office

Kansas City District

Schedule

Request for Assistance:	Aug. 26, 2011
Damage Survey Report:	Oct. 28, 2011
Award Date:	June 21, 2012
Notice to Proceed Date:	June 28, 2012
Contract Duration:	90
Contract Original Completion Date:	Sept 26, 2012
Contract Current Completion Date:	Sept 26, 2012
Estimated Completion Date:	Sept 26, 2012


Progress

% Complete Actual:	70%
% Complete Schedule:	70%
Construction Contract Placement:	

Funding

Funds Source:	FCCE – Rehabilitation
Award Contract Amount:	
Current Contract Amount:	
Pending MOD Amount:	

Project: Baltimore Cherry Miles Ray Henrietta Crooked River Miles: 300.3 to 302.2

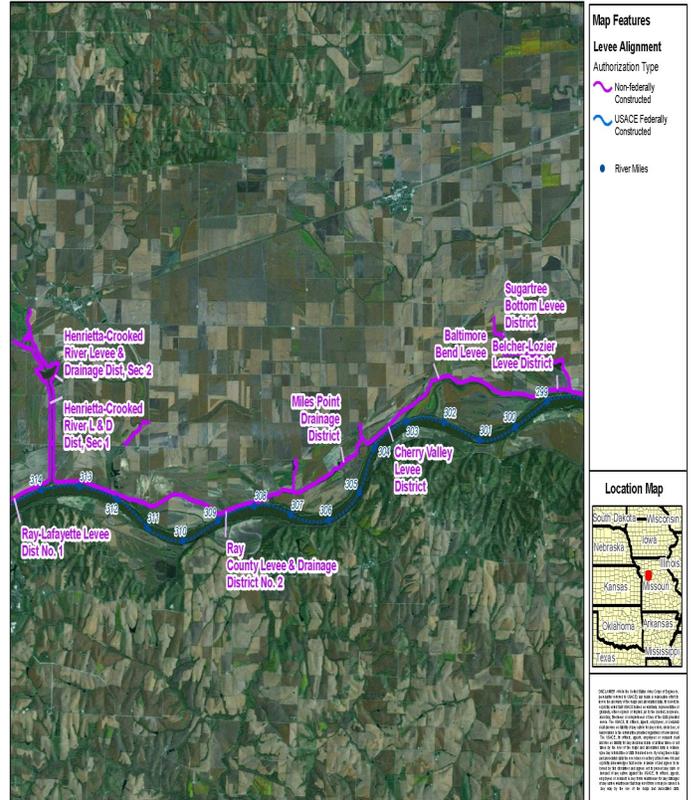

Scope of work

Ray County Levee Unit is part of the levee system with Belcher-Lozier, Cherry Valley, Miles Point, Henrietta-Crooked River, Section 2 and Baltimore Bend County Levee Units. Repairs consist of drainage structure and erosion repair.

Current Progress

Widel has completed installation of drainage structure to include flap-gate. Seeding/mulching remains.

Photos
